



# Newton North High School

## Project Areas by function / Current Construction Activity – 5/15/09

### Site work – General Items:


Gravel, grading and install light pole bases at north parking lot  
Grading work at tennis court area.

### Pool/Small gym (B) –

Concrete foundations and steel erection is complete - complete  
Concrete floors - level 1 and 2 complete  
Plumbing roof drainage piping – ongoing – 90% complete  
Underground plumbing – ongoing – 10% complete  
Fireproof paint at structural steel – ongoing- 70% complete  
Exterior Masonry – started 5/11/09  
Permanent roof to start 6/1/09 +/-

### Academic (C)

Concrete floors: All levels - complete.  
Interior spray on fireproofing – level 2 & 3 & 4 – completed. Ground level – 80% complete – completion will occur subsequent to low roofing installation  
Rough Mechanical/plumbing/ ductwork/electrical installation- Level 4 – 88% complete, Level 3 – 85% complete, Level 2 – 75% complete, Level 1 – 25 % complete.  
Interior metal studs – scheduled to start – week of 5/18/09.  
Interior Masonry – level 4 – 98% complete, level's 2 and 3 – 98% complete. Ground level 95% complete  
Exterior Masonry – ongoing - 90% complete  
Exterior framing, sheathing – 99% complete – exterior waterproofing ongoing – 90% complete  
Permanent Roof Insulation work (except at low roof) – 100% complete.  
Stair #5 - complete

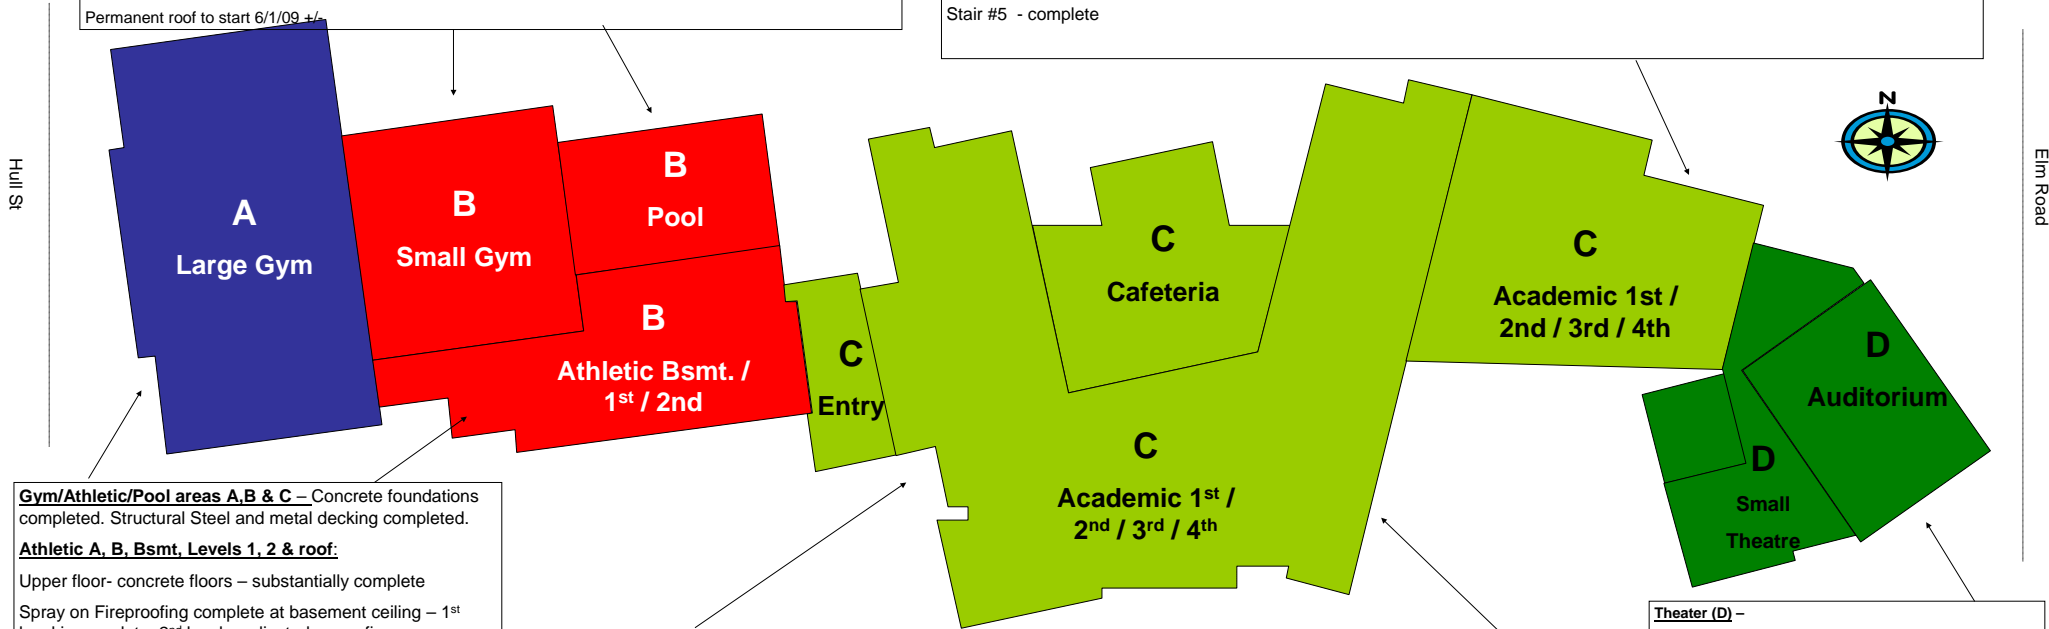

**Gym/Athletic/Pool areas A,B & C** – Concrete foundations completed. Structural Steel and metal decking completed.

### Athletic A, B, Bsmt, Levels 1, 2 & roof:

Upper floor- concrete floors – substantially complete  
Spray on Fireproofing complete at basement ceiling – 1<sup>st</sup> level is complete, 2<sup>nd</sup> level predicated on roofing  
Plumbing rough in piping complete at basement locker rooms – 100% complete  
Interior masonry – level 1- ongoing- 85 % complete, basement – ongoing – 60%. Level 2- will start on 5/16/09 +/-.  
Roof parapet framing ongoing– 95%  
Wall framing and sheathing ongoing – 95%  
Window flashings/Exterior vapor barrier – started 5/7/09  
Stair #1 – started – 60% complete  
Permanent roof insulation installation – Athletic “B” roof – completed week of 5/11/09, Athletic A – scheduled for 5/18/09.  
Elevator A – started on 5/11/09.

### Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- 99% complete. Level 3 -98% complete, Level 2 – 98% complete, Level 1 -88% complete. Continuance of level 1 contingent on cafeteria roof installation.  
Exterior framing, sheathing – ongoing – 98% complete / Exterior flashings and waterproof barrier ongoing – 95% complete.  
Interior metal stud framing – 94% complete. 3<sup>rd</sup> floor ready for drywall installation - start contingent on window installation – tentatively scheduled to start – week of 5/25/09.  
Window delivery – ongoing – installation at south elevations started 5/4/09.  
Interior masonry partitions – ongoing – 98% complete.  
Exterior Masonry – Brick work started week of 2/2/09 – ongoing – 92% complete  
Permanent roof insulation / Temporary roof – 100% of main complete – permanent roofing to be installed mid June 2009.  
Culinary Arts – walk in coolers being delivered week of 5/22/09 +/-  
Elevator B – ongoing – elevator platform complete – elevator entrances started  
Removal of temporary stair tower – scheduled for 6/18/09.

### Theater (D) –

Perimeter concrete foundations and structural steel and small theater floor concrete - complete  
Miscellaneous concrete Control room, stage and orchestra pit walls complete 100%. Second floor concrete complete – orchestra pit floor slab complete, stage slab floor scheduled for 5/20/09.  
Exterior Masonry at large theater stage perimeter – starting week of 5/11/09.  
Underground piping work - complete.  
Permanent roofing @ small theater – start 5/14/09 +/-  
Fireproofing paint @ structural steel– ongoing– 90% complete. Spray on Fireproofing awaiting roof installation  
HVAC equipment (chiller) set in place - week of 4/6, piping ongoing  
Masonry - Exterior – started 4/13 – ongoing – 30% complete. Masonry – Interior- ongoing – 25% complete  
Rooftop HVAC Units – will be set in place 5/20/09 +/-
