

Newton North High School

Project Areas by function / Current Construction Activity – 7/31/09

Site work – General Items


Screening / distributing topsoil
 Ceremonial Drive - drainage complete – site electrical started
 Stadium concrete retaining wall – 90% complete footings, 80% walls complete, Bleacher footing excavation started.
 Miscellaneous site grading / site utility work / loam screening - . Access road binder course paved 7/16/09
 Elm Road sidewalk preparation ongoing – concrete placement 8/5/09

Pool/Small gym (B) –

Plumbing roof drainage piping – complete
 Underground plumbing – 80% complete
 Small gym – concrete slab preparation started – concrete placement –week of 8/10/09
 Exterior Masonry (CMU) – 100 % - brick – 95% complete
 Permanent roof- ongoing – 95 % complete
 Swimming pool excavation with pool piping – started - 70% complete

Academic (C)

Interior spray on fireproofing – level 2 & 3 & 4 – completed. Ground level – 80% complete – completion will occur subsequent to low roofing installation.
 Rough Mechanical/plumbing/ ductwork/electrical installation- Level 4 – 100% complete, Level 3 – 98% complete, Level 2 – 98% complete, Level 1 – 65 % complete.
 Interior metal studs – level 2 – 100% complete, level's 3 and 4 – 99% complete. Level 2 90% complete, ground floor started
 Interior drywall – started 6/26/09. Lev 3 – 98% complete, Lev 4– 75% complete, Lev 2 to start wk of 8/10/09.
 Interior Masonry – Levels 4, 3, & 2 – 100% complete.
 Prime Painting – Level 3 – 85%, Level 4 – 45%, Level 2 – 20%
 Exterior Masonry (Brick) - 99% complete
 Exterior framing, sheathing – 99% complete – exterior waterproofing – 98% complete
 Permanent Roof Insulation work (except at low roof) – 100% complete.
 Stair #5 - complete
 Window installation – ongoing - 95% complete / Curtainwall framing & glazing – 35%

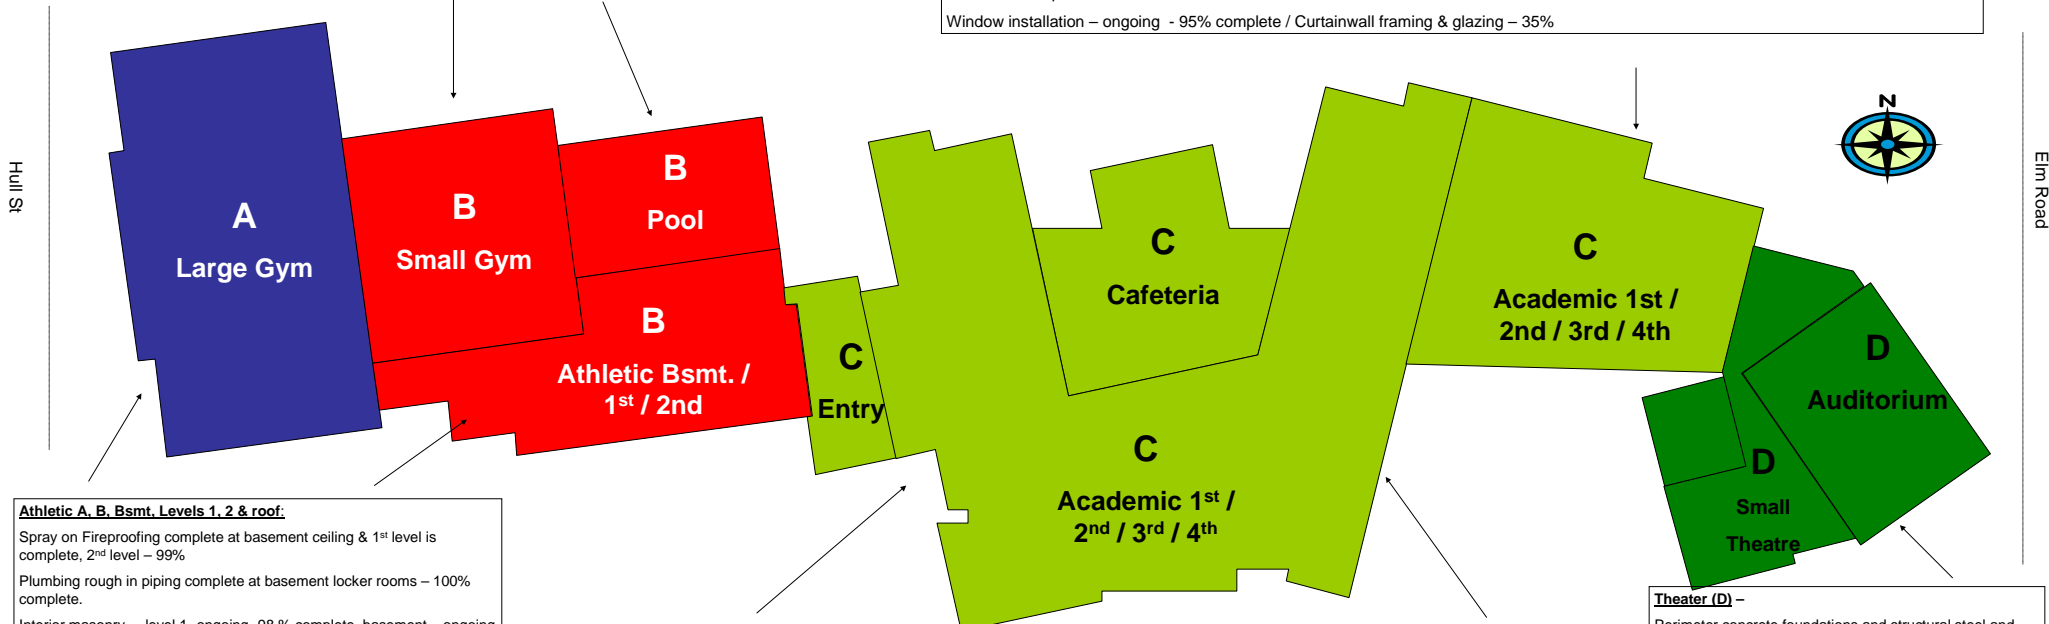

Athletic A, B, Bsmt. Levels 1, 2 & roof:

Spray on Fireproofing complete at basement ceiling & 1st level is complete, 2nd level – 99%
 Plumbing rough in piping complete at basement locker rooms – 100% complete.
 Interior masonry – level 1- ongoing- 98 % complete, basement – ongoing – 100%. Level 2 – ongoing – 98% complete. Large gym perimeter – ongoing -97% complete.
 Exterior Brick – west side of "A" – 90% complete, east side of "A" – 70%
 Roof parapet framing ongoing– 100% complete
 Wall framing and sheathing ongoing – 98%
 Window flashings/Exterior vapor barrier – ongoing – 80%
 Stair #1 – 100% complete – awaiting permanent railings
 Elevator A – platform complete – elevator cab construction ongoing.
 Mechanical/Electrical/Plumbing – Overhead piping at basement level – 88% complete
 Roof Top HVAC units – set in place on 6/22 – piping work ongoing.
 Interior Metal Stud framing – started 7/6/09, 65% complete
 Natatorium seating area – Masonry – 92%, concrete – 78% complete

Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- 99% complete. Level 3 -99% complete, Level 2 – 99% complete, Level 1 -92% complete.
 Continuance of level 1 contingent on cafeteria roof installation.
 Exterior framing, sheathing - 99% complete / Exterior flashings and waterproof barrier ongoing – 99% complete.
 Drywall – level 3 -,98% complete, level 4- 80%, level 2 – 20%.
 Prime Painting – level 3 – 95% complete, level 4– 75% complete, level 2 – 40% complete, level 1 15% complete. 1st finish coat started @ Level 3
 Window delivery/installing – ongoing – 87%
 Curtain Wall – ongoing – 35%
 Interior masonry partitions – ongoing – 99% complete – masonry punch list work ongoing
 Exterior Masonry – Brick work started week of 2/2/09 – 99% complete – precast feature - started
 Permanent roof insulation / Temporary roof – 100% of main roof complete. Cafeteria permanent roof – 75% complete
 Culinary Arts/ Kitchen – Kitchen exhaust hoods installed week of 5/18/09. Walk in cooler at culinary arts installed 6/2/09 – concrete topping slab place 7/30/09
 Elevator B – ongoing – elevator entrances completed – . Elevator C platform complete.
 Preparatory work for metal panels – furring/insulation – ongoing – 65% complete – Metal Panel work started – 15%
 Acoustic ceiling grid – started at level 3.

Theater (D) –

Perimeter concrete foundations and structural steel and small theater floor concrete - complete
 Miscellaneous concrete Theater – tiered seating platform concrete ongoing – 95% complete.
 Exterior Masonry at large theater perimeter – 95% complete. Exterior masonry is complete at small theater. Brick- south elevation – 100% complete. East elevation small theater – brick complete
 Water proofing small theater – 100% complete.
 Interior Masonry at small theater 98% complete, large theater 90% complete – ready for brick exterior to start.
 Permanent roofing @ small theater – temporary roof installed – permanent roof scheduled week of 8/3/09
 Fireproofing paint @ structural steel– ongoing– 100% complete. Spray on Fireproofing – 75%
 HVAC equipment (chiller) is in place. Chiller pumps delivered week of 5/25/09, piping at pump room – 95% complete – distribution piping – 40%.
 Overhead steel catwalk work ongoing – 80% complete
