

Newton North High School

Project Areas by function / Current Construction Activity – 9/11/09

Site work – General Items


Screening / distributing topsoil – completed – spreading of loam will be by landscaper
 Ceremonial Drive - drainage complete – site electrical started – 40% complete. Site wall excavation has started.
 Stadium concrete retaining wall – footings completed, walls - 95% complete, Bleacher concrete footings – 75% complete
 Tennis court retainings wall footings – started / Hull St stairway – to start on 9/17/09
 Elm Road . Connector Road - concrete sidewalk / curb – 99% - fence relocated / street cleaned for start of school

Pool/Small gym (B) –

Concrete floor – complete - placed on 08/19/09
 Exterior Masonry (CMU) – 100 % - brick – 98% complete
 Permanent roof- ongoing – 98 % complete – miscellaneous flashings etc remaining to be installed
 Swimming pool formwork 95% complete – gunite installation – started.
 Prime painting work at small gym – walls and ceiling – completed.
 Stainless steel shower trench drains – 90% complete.
 Elevated Pool seating area – concrete and masonry completed

Academic (C)

Interior spray on fireproofing – level 2 & 3 & 4 – completed. Ground level – 90% complete – completion will occur subsequent to low roofing installation. Roofing at low roofs - 100% complete.
 Rough Mechanical/plumbing/ ductwork/electrical installation- Level 4 – 100% complete, Level 3 – 98% complete, Level 2 – 98% complete, Level 1 – 80 % complete.
 Interior metal studs – level 2 – 100% complete, level's 3 and 4 – 99% complete. Level 2 98% complete, ground floor - 60%
 Interior drywall – started 6/26/09. Lev 3 – 98% complete, Lev 4– 90% complete, Lev 2 - 50 % complete.
 Interior Masonry – Levels 4, 3, & 2 – 100% complete, Level 1 90% complete.
 Prime Painting – Level 3 – 95%, Level 4 – 85%, Level 2 – 75%, Level 1 – 40%
 Exterior Masonry (Brick) - 99% complete
 Exterior framing, sheathing – complete – exterior waterproofing –complete
 Permanent Roof Insulation work (except at low roof) – 100% complete. Low roof membrane installation – 80%
 Ceiling grid installation - 15%
 Window installation – ongoing - 100% complete / Curtain wall framing & glazing – 70%

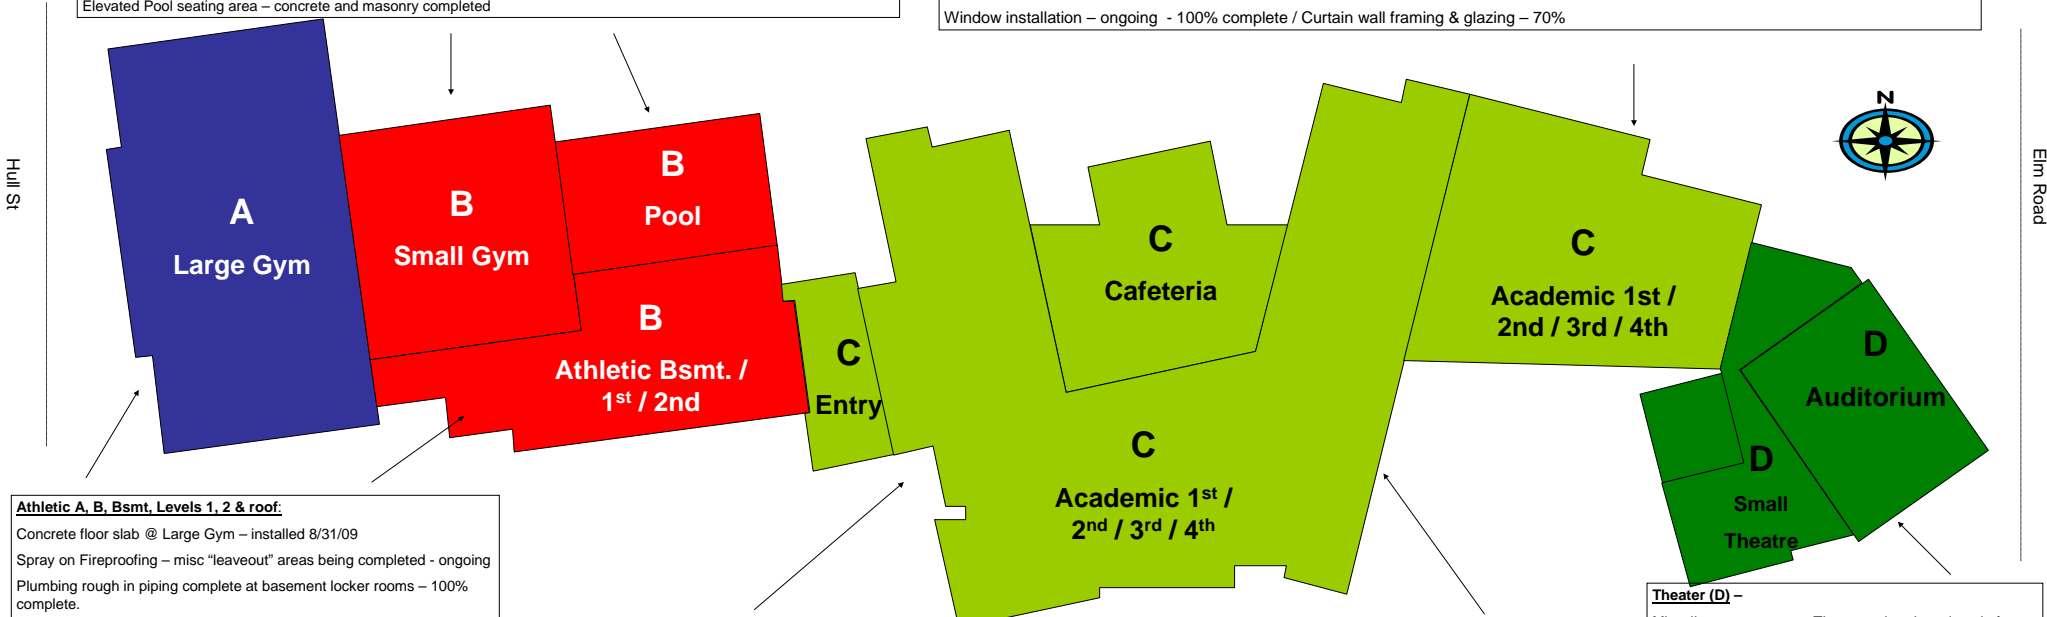

Athletic A, B, Bsmt, Levels 1, 2 & roof:

Concrete floor slab @ Large Gym – installed 8/31/09
 Spray on Fireproofing – misc "leavout" areas being completed - ongoing
 Plumbing rough in piping complete at basement locker rooms – 100% complete.
 Interior masonry – level 1- ongoing- 98 % complete, basement – ongoing – 100%. Level 2 – ongoing – 98% complete. Large gym perimeter – ongoing -99% complete.
 Exterior Brick – west side of "A" – completed week of 8/10, east side of "A" – 99%
 Roof parapet framing ongoing– 100% complete
 Wall framing and sheathing ongoing – 98%
 Window flashings/Exterior vapor barrier – completed
 Stair #1 – 100% complete – permanent railings – 25% complete
 Mechanical/Electrical/Plumbing – Overhead piping at basement level – 95% complete
 Roof Top HVAC units – set in place on 6/22 – piping work ongoing.
 Interior Metal Stud framing – started 7/6/09, 82% complete
 Natatorium seating area – Masonry – 95%, concrete – 95% complete

Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- 99% complete. Level 3 -99% complete, Level 2 – 99% complete, Level 1 -94% complete. Continuance of level 1 contingent on cafeteria roof installation.
 Exterior framing, sheathing - 99% complete / Exterior flashings and waterproof barrier ongoing – 99% complete.
 Drywall – level 3 -,98% complete, level 4- 90%, level 2 – 87%, Level 1 – 40%.
 Prime Painting – level 3 – 95% complete, level 4– 95% complete, level 2 – 70% complete, level 1 40% complete. 1st finish coat started @ Level 3 and is 70% complete.
 Window delivery/installing – ongoing – 99% / Curtain Wall installation - ongoing – 70% - Cafeteria large curtainwall framing at west elevation - started
 Interior partitions – ongoing – 99% complete – masonry punch list work ongoing / misc cafeteria/main st soffits and drywall - ongoing
 Exterior Masonry – Brick work started week of 2/2/09 – 99% complete – precast concrete base – 84%
 Permanent roof insulation / Temporary roof – 100% of main roof complete. Cafeteria permanent roof – 99% complete – skylights installed
 Culinary Arts/ Kitchen – Kitchen exhaust hoods installed week of 5/18/09. Walk in cooler at culinary arts installed 6/2/09 – concrete topping slab completed – 7/30/09
 Elevator B – ongoing – elevator entrances completed – . Elevator C platform complete – interior cab completed 08/10/09
 Preparatory work for metal panels – furring/insulation – 95% complete – Metal Panel work started – 70%
 Acoustic ceiling grid – level 3 – 95%, level 4 – 75%, Level 2 – 10%
 Electrical devices / trimout -ceilings & light fixtures – level 3 – 15%
 Science lab/classroom casework – started at Level 4 – 50% complete installation – deliveries ongoing. Mechanical/Plumbing/Electrical hookups started

Theater (D) –

Miscellaneous concrete Theater – tiered seating platform concrete ongoing – completed.
 Exterior Masonry at large theater perimeter – 95% complete. Exterior masonry is complete at small theater. Brick- south elevation – 100% complete. East elevation small theater – brick complete. Exterior waterprf'g 80%.
 (temporary work platform at theater – installed – overhead MEP at theater 40% complete.
 Interior Masonry at small theater 100% complete, large theater 100% complete – ext brick is 85% complete.
 Permanent roofing @ small theater – temporary roof installed – permanent roof at stage completed.
 Fireproofing paint @ structural steel– ongoing– 100% complete. Spray on Fireproofing – 80%
 HVAC equipment (chiller) is in place. Chiller pumps delivered week of 5/25/09, piping at pump room – 95% complete – distribution piping – 80%.
 Overhead steel catwalk work ongoing – 80% complete
