



Newton North High School

Project Areas by function / Current Construction Activity – 01/15/10

Site work – General Items


Football field/track – subbase preparation - completed, drainage – 99% / Bleacher installation – 99% - paving-complete
 Perimeter sidewalks ongoing – 60% - placements continuing weather dependant
 Tennis court retaining wall- completed / Tennis Ct lighting bases – complete , Hull St concrete stairway - complete - final sub grade prep - substantially completed
 Loading Dock – structural steel erection started 1/14/10
 Grading and granite curb – Ceremonial Drive – ongoing – curb 95%, roadway grading 100% - paving completed 12/3/09.
 NOTE – Exterior work to largely resume – Spring 2010

Pool/Small gym (B) –

Perimeter roof flashings/ roof edge copings 70%
 Swimming pool gunite installation completed – pool water test complete
 Swimming pool perimeter slab – placed on 1/14/10
 Prime painting and 1st finish coat painting at small gym – walls and ceiling – completed.
 Misc interior masonry work in pool shower area – 98% compl. / Plumbing piping for pool area showers/baths – 98% compl
 Athletic Equip – basketball backboards, divider, scoreboards, public address system - completed - small gym – same work ongoing in lrg gym – all 95% complete

Academic (C)

Classroom casework installation – level 4 - complete, level 3 – complete, level 2 – 95%, level 1 – 55%
 Locker installation – level 4 – 99% complete%, level 3 – 95%. Level 2 – 60%
 Rough Mechanical/plumbing/ ductwork/electrical installation- Level 4 – 100% complete, Level 3 – 99% complete, Level 2 – 98% complete, Level 1 – 98 % complete. MEP above ceiling punch lists being completed ahead of ceiling time installations
 Interior metal studs – level 2 – 100% complete, level's 3 and 4 – complete. Level 2 complete, Lev 1 - 95%
 Interior drywall – started 6/26/09 @ Lev 3 – complete, Lev 4– complete, Lev 2 - complete, Lev 1- 95%
 Prime Painting – Level 3 – 100%, Level 4 – 100%, Level 2 – 100%, Level 1 – 99% - Finish painting ongoing.
 Exterior Masonry (Brick) - complete / exterior metal panels – 99% complete
 Permanent Roof Insulation work (except at low roof) – completed. Lower roof membrane complete
 Ceiling grid installation - 98% overall
 Window installation – ongoing - 100% complete / Curtain wall framing & glazing – 98%
 Operable partitions – framing and track installed
 Overhead doors (exterior) – completed / Interior doors/frames and hardware- ongoing
 Resinous flooring – 85% overall

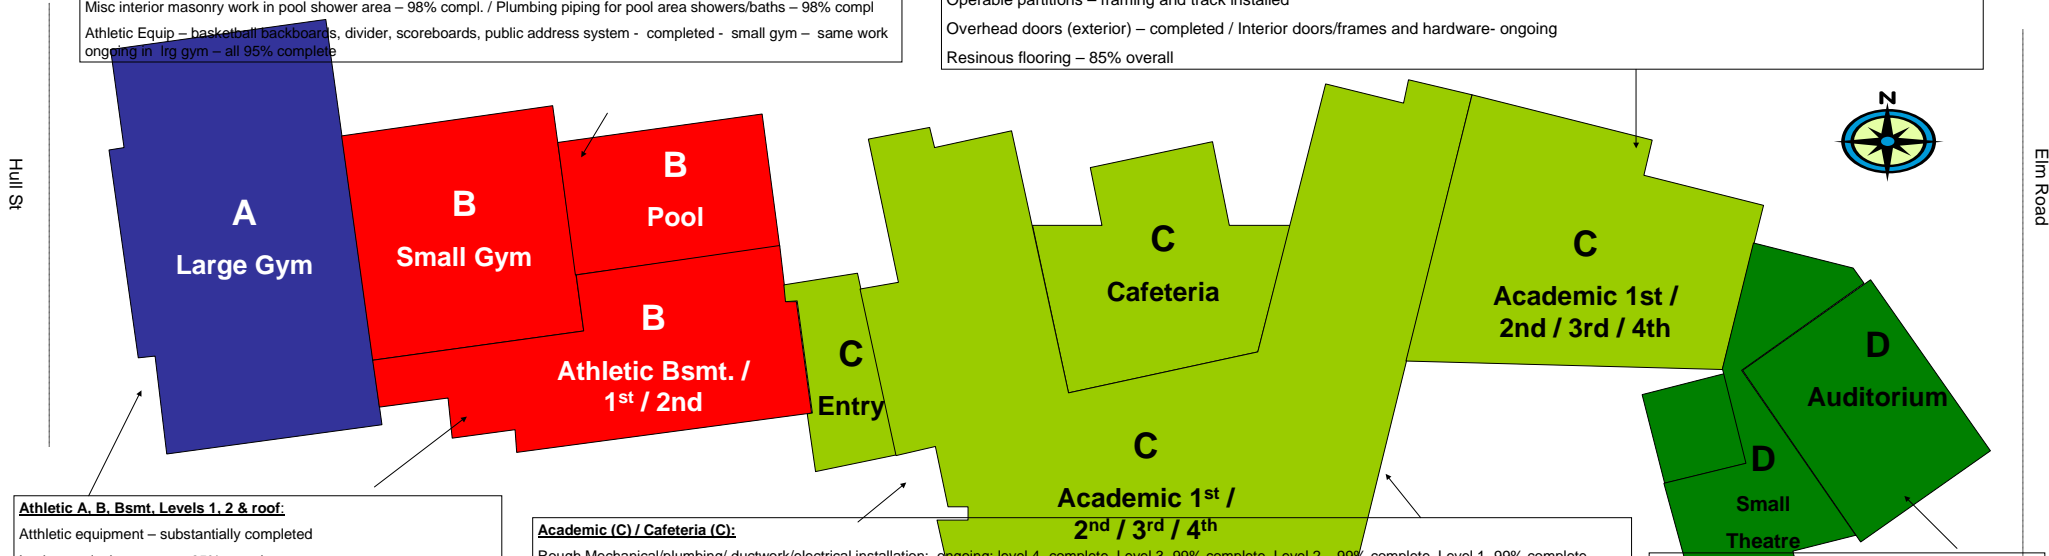

Athletic A, B, Bsmt. Levels 1, 2 & roof:

Athletic equipment – substantially completed
 Lockers at locker rooms – 95% complete
 Stair #1 – 100% complete – permanent railings –complete
 Mechanical/Electrical/Plumbing – Overhead piping at basement level - substantially complete – Overhead piping large gym – 98% complete
 Roof Top HVAC units – set in place on 6/22 – piping work 98% complete
 Interior Metal Stud framing – complete / drywall 95% complete
 Natatorium seating area – concrete and masonry work completed
 Misc drywall @ Child care - complete
 Mechanical overhead piping at large gym – 95% complete.
 Kalwall windows – completed 12/8/09
 Curtain wall – ongoing – 95% complete
 Ceiling grid – basements – ongoing 95%, 1st floor – 80%
 Low permanent roof at elevator – completed.
 Elevator - final adjustments – ongoing for elevator inspection in mid Jan
 Resinous flooring – ongoing – 60%
 Wood Flooring delivered – large gym - installation to start 1/22/10

Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- complete, Level 3 -99% complete, Level 2 – 99% complete, Level 1 -99% complete.
 Drywall – level 3 - complete, level 4- complete, level 2 – complete, Level 1 – 99%.
 Prime Painting – level 3 – complete, level 4– complete, level 2 – complete, level 1 -98% complete. 1st finish coat started @ Level 3 and 4 -complete – 1st coat finish painting level 2 -98% – misc prime painting ongoing level 1-98%
 Window /installation– ongoing – 99% / Curtain Wall installation - ongoing – 95% - Cafeteria large curtain wall glazing – 98%
 Main st soffits and drywall – ongoing – 98%
 Permanent roofing roof – main roof complete. Cafeteria permanent roof – complete. Perimeter roof copings – 60%
 Elevator B and C -- temporary inspection certificate completed at elevator B.
 Exterior metal panel work – ongoing- 90%
 Acoustic ceiling grid – level 3 – 100%, level 4 – 100%, Level 2 – 100% , Level 1 – 90% - install ceiling tile – level 4 – complete, Level 3 – 98%, level 2 – 90%, lev 1 - 70%
 Electrical devices / trimout -ceilings & light fixtures – level 3 – 90%, level 4 – 95%, level 2 – 85%, Lvl 1- 30%
 Science lab/classroom casework – Level 4 – 98% , Level 3 – 95% complete, level 2- 60%, Level 1 – 50%. Mechanical/Plumbing/Electrical hookups following installation.
 Resinous Flooring – level 4 – complete, level 3 – 95% - level 2 – 70% - plumbing fixtures ongoing – level 4, 3, and 2, and 1 - 85%
 Quarry Tile flooring at kitchen started 1/1. / QT at culinary arts complete. Food Service equipment deliveries – ongoing.
 Vinyl flooring – level 4- 90%, level 3 – 65%, level 2 – 40%, level 1 – 10%
 Locker installation – Level 4 – 99%, level 3 – 95%, Lvl 2 – 80%, Lvl1 - 80%
 Wood door / hardware installation – Lvl 4 – 85%, level 3 – 40% / Marker/tack board started – all areas – 90% / coiling doors all areas – completed

Theater (D) –

Misc prime painting at small theater and surrounding areas – completed, finish painting ongoing outside large theater (temporary work platform has been removed – overhead MEP at theater- complete. overhead millwork –completed.
 Interior Masonry at small theater 100% complete, large theater 100% complete – ext brick is 100% complete.
 Fireproofing paint @ structural steel completed. Spray on Fireproofing –complete – misc patching ongoing
 HVAC equipment (chiller) is in place, piping at pump room – 98% complete – distribution piping – 99%.
 Theater lighting & controls rough ins – ongoing – 85%
 Overhead steel catwalk /spiral stairs work - complete
 Interior misc metal railings – 25%
 Curtain wall @ Theater entry – 99% complete
 Theater rigging - 95%
 Small theater drywall – complete
 Wheelchair lifts – started 1/11.
 Theater interior finishes – acoustical panel framing – started.
