



Newton North High School

Project Areas by function / Current Construction Activity – 02/26/10

Site work – General Items


Football field/track – subbase preparation - completed, drainage – 99% / Bleacher installation – 99% - paving-complete
 Perimeter sidewalks ongoing – 65% - placements continuing weather dependant
 Tennis court retaining wall- completed / Tennis Ct lighting bases – complete , Hull St concrete stairway - complete - final sub grade prep - substantially completed
 Loading Dock – structural steel erection completed – misc steel detailing nearly finished. Anticipate slab placement – mid Feb +/-
 Grading and granite curb – Ceremonial Drive – ongoing – curb 95%, roadway grading 100% - paving completed 12/3/09.
 NOTE – Exterior work to largely resume – Spring 2010

Pool/Small gym (B) –

Perimeter roof flashings/ roof edge copings 90%
 Natatorium – Overhead mechanical, electrical, painting – completed – work platform removed
 Pool tile preparation –started / Pool equipment installation nearing completion
 Pool Locker room finishes (tile)- 90% complete
 Prime painting, 1st and 2nd finish coat painting at small gym – walls and ceiling – completed.
 Small Gym - Wood flooring installation – 50%
 Athletic Equip – basketball backboards, divider, scoreboards, public address system - completed at both gyms

Academic (C)

Classroom casework installation – level 4 - complete, level 3 – complete, level 2 – complete, level 1 – 94%
 Locker installation – level 4 – 100% complete%, level 3 – 99%. Level 2 – 95%
 Rough Mechanical/plumbing/ ductwork/electrical installations- all rough in activities completed – air balancing and started. System and equipment commissioning started.
 Interior metal studs – level 2 – 100% complete, level's 3 and 4 – complete. Level 2 complete, Lev 1 - complete
 Interior drywall – started 6/26/09 @ Lev 3 – complete, Lev 4– complete, Lev 2 - complete, Lev 1- complete
 Prime Painting – Level 3 – 100%, Level 4 – 100%, Level 2 – 100%, Level 1 – 99% - Finish painting ongoing and nearing completion in all areas of Area C
 Exterior Masonry (Brick) - complete / exterior metal panels – 99% complete
 Permanent Roof Insulation work (except at low roof) – completed. Lower roof membrane complete- perimeter copings ongoing
 Ceiling grid installation - 98% overall / ceiling tile - 90% complete
 Window installation – ongoing - 100% complete / Curtain wall framing & glazing – 100%. Entry doors nearly completed
 Overhead doors (exterior) – completed / Interior doors/frames and hardware- ongoing
 Resinous flooring – 100% overall
 Resilient flooring/vinyl sheet goods – 88% overall complete
 Architect Punch list process – scheduled to start – 3/1/10 @ Level 4

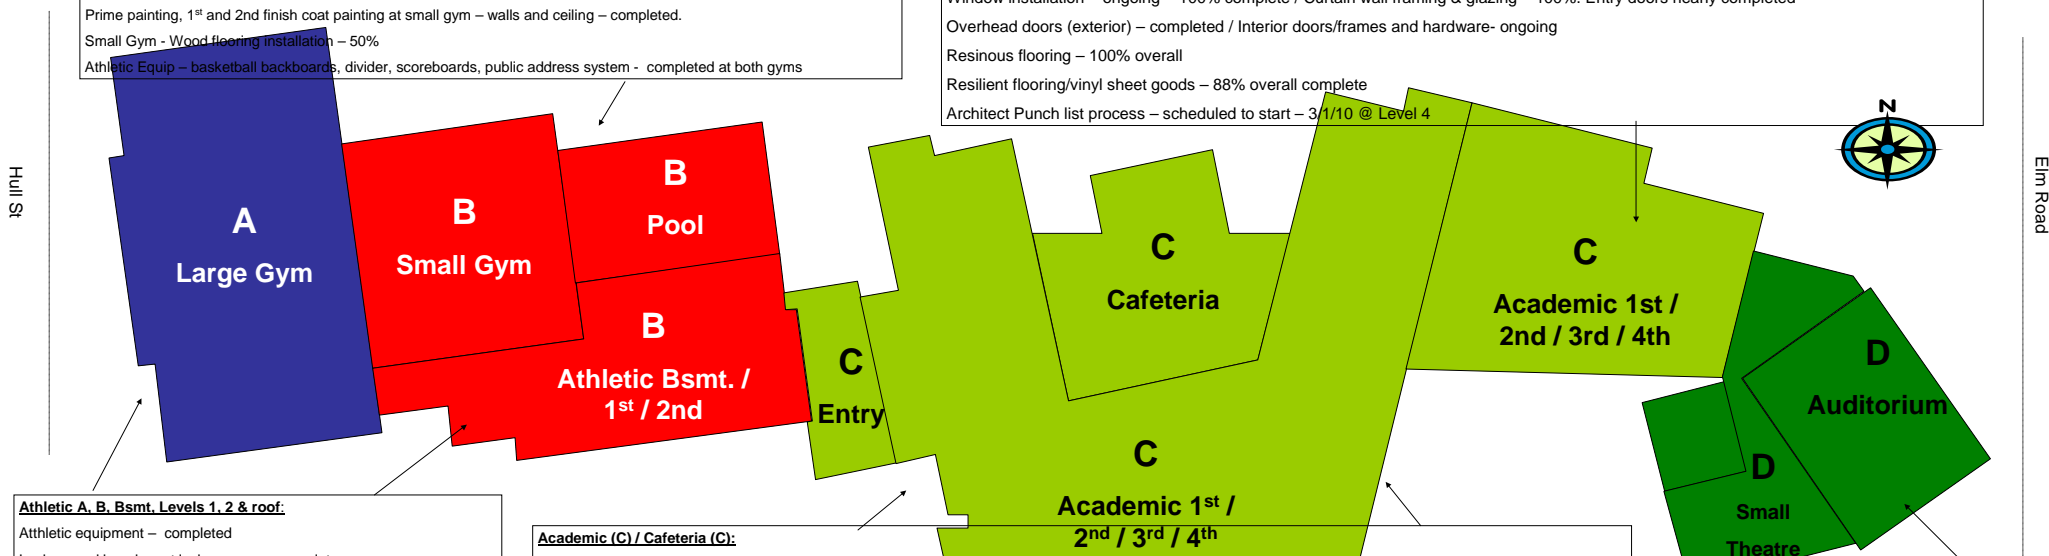

Athletic A, B, Bsmt, Levels 1, 2 & roof:

Athletic equipment – completed
 Lockers and benches at locker rooms – complete
 Large gym – synthetic floor to start early February, floor prep 80% completed
 Mechanical/Electrical/Plumbing – Overhead piping at basement level - substantially complete – Overhead piping large gym – 100% complete
 Roof Top HVAC units – set in place on 6/22 – piping work 99% complete
 Interior Metal Stud framing / drywall complete
 Natatorium seating area – concrete and masonry work completed
 Misc drywall @ Child care - complete
 Mechanical overhead piping at large gym – 99% complete.
 Kalwall windows – completed 12/8/09
 Curtain wall – ongoing – 100% complete, aluminum entrances near complete.
 Ceiling grid – basements – ongoing 99%, 1st floor – 99%, 2nd floor – 90%
 Low permanent roof at elevator – completed.
 Elevator - temp use certificate received
 Resinous flooring – ongoing – 95%
 Ceramic Tile –basement – 40%
 Synthetic flooring at dance room – completed.
 Photovoltaic installation - started

Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- complete. Level 3 -100% complete, Level 2 – 99% complete, Level 1 -99% complete.
 Drywall – level 3 - complete, level 4- complete, level 2 – complete, Level 1 – complete
 Prime Painting – level 3 – complete, level 4– complete, level 2 – complete, level 1 100% complete. Final coat painting – ongoing all areas.
 Window /installation– complete / Curtain Wall installation - ongoing – 100% - Cafeteria large curtain wall glazing – complete
 Main st soffits and drywall – completed
 Permanent roofing roof – main roof complete. Cafeteria permanent roof – complete. Perimeter roof copings – 88%
 Exterior metal panel work – ongoing- 97%
 Acoustic ceiling grid – level 3 – 100%, level 4 – 100%, Level 2 – 100% , Level 1 – 98% - install ceiling tile – level 4 – complete, Level 3 – 98%, level 2 – 95%, lev 1 - 94%
 Electrical devices / trimout -ceilings & light fixtures – level 3 – 99%, level 4 – 98%, level 2 – 98%, Lvl 1- 90%
 Science lab/classroom casework – Level 4 – 100% , Level 3 – 99% complete, level 2- 90%, Level 1 – 88%. Mechanical/Plumbing/Electrical hookups following installation.
 Resinous Flooring – level 4 – complete, level 3 – 100% - level 2 – 100%, level 1 – 90% - plumbing fixtures ongoing – level 4, 3, and 2, and 1 - 90%
 Quarry Tile flooring at kitchen-completed. / QT at culinary arts complete. Food Service equipment deliveries – 95% Culinary Arts, 60% at main kitchen.
 Vinyl flooring – level 4- 100%, level 3 – 95%, level 2 – 90%, level 1 – 85%
 Locker installation – Level 4 – complete, level 3 – 100%, Lvl 2 – 99%, Lvl1 - 95%
 Wood door / hardware installation – Lvl 4 – 100%, level 3 – 100%, lev 2 – 95%, lv 1 – 80% / Marker/tack board started – all areas – 90% / coiling doors all areas – completed
 Carpet installation @ library – 90% complete

Theater (D) –

Misc prime painting and finish at small theater and surrounding areas – completed, finish painting ongoing all areas
 Concrete floor staining - complete
 Acoustical wall panel frames -installed
 HVAC equipment (chiller) is in place, piping at pump room – 99% complete – distribution piping – 99%.
 Theater lighting & controls rough ins – ongoing – 99%
 Overhead steel catwalk /spiral stairs work – complete
 HP lifts – 95% installed
 Interior misc metal railings –completed
 Curtain wall @ Theater entry – 100% complete
 Theater rigging - 98%
 Theater seating – 85% complete
 Wood flooring @ small theater – started – 20% complete
 Main stage flooring/millwork – started – 40% complete
