



# Newton North High School


## Project Areas by function / Current Construction Activity – 4/17/09

### Athletic/Pool/Sm gym (B) –

Concrete foundations - complete  
 Structural Steel erection – substantially complete – topping off ceremony held 12/12/08.  
 Metal decking – 100% complete  
 Temporary weather protection – removal – week of 4/6/09  
 Concrete floor - level 1 and 2 complete  
 Plumbing roof drainage piping - started

### Academic (C)

Concrete floors: All levels - complete.  
 Interior spray on fireproofing – level 2 & 3 – completed. Underside of roof fireproofing – 100% complete. Ground level – 80% complete.  
 Underground piping/utilities below level 1 are complete  
 Rough Mechanical/plumbing/ ductwork/electrical installation- Level 4 – 45% complete, Level 3 – 55% complete, Level 2 – 35% complete, Level 1 – 20 % complete.  
 Interior Masonry - level's 2 and 3 – 98% complete. Ground level 90% complete  
 Exterior framing, sheathing – ongoing – 97% complete.  
 Permanent Roof Insulation work – 100% complete.  
 Stair #5 installation has started – 4/10/09  
 Winter weather protection and temporary heating – removal nearly completed

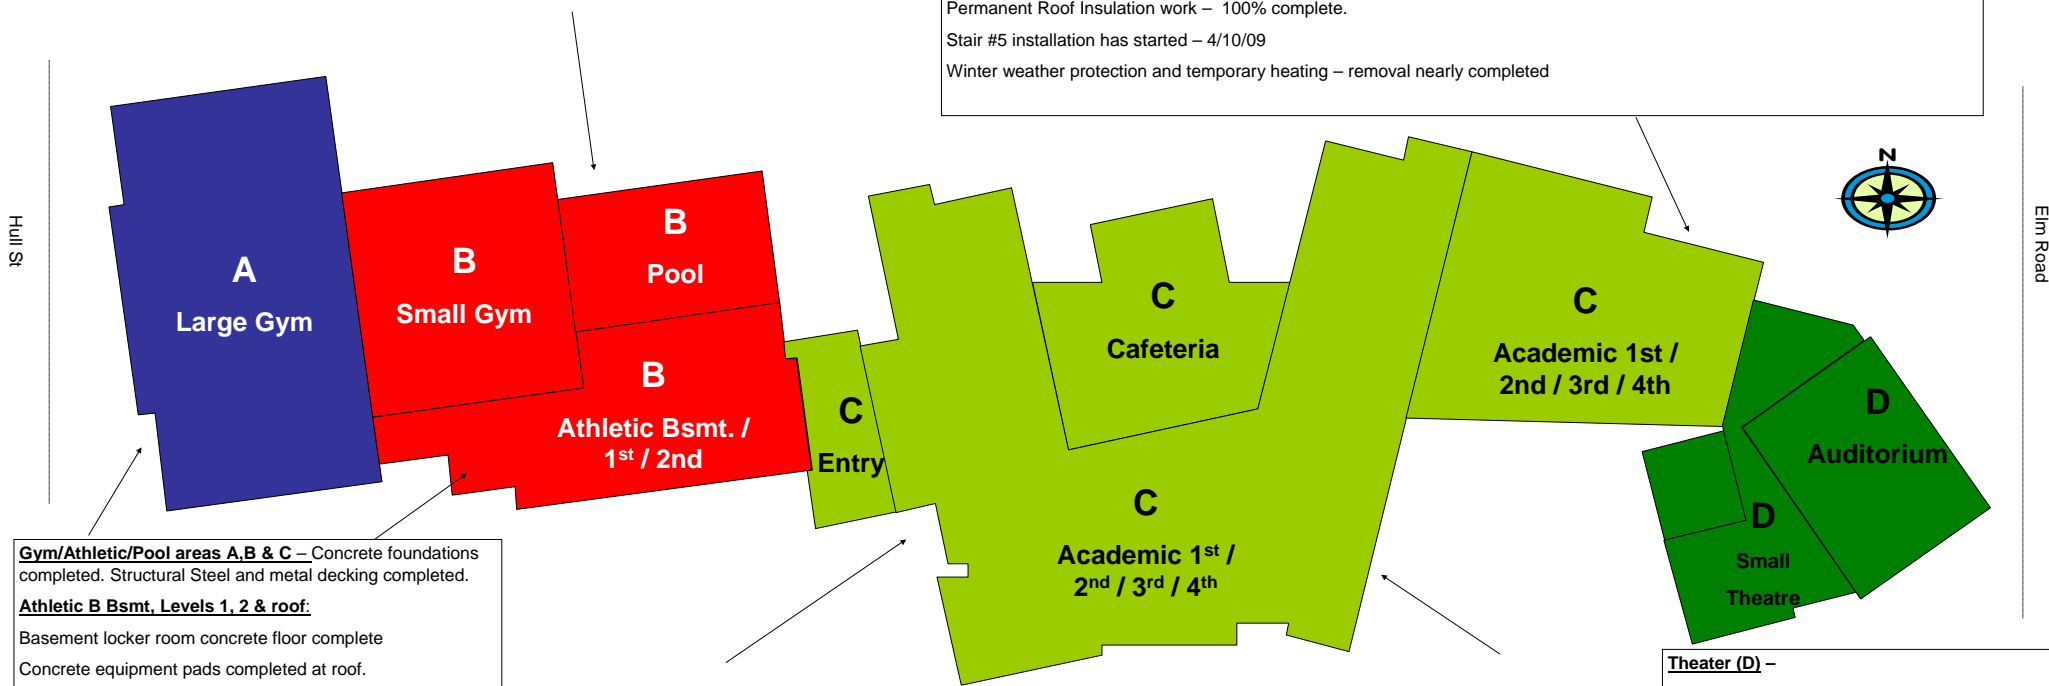

**Gym/Athletic/Pool areas A,B & C –** Concrete foundations completed. Structural Steel and metal decking completed.

### Athletic B Bsmt, Levels 1, 2 & roof:

Basement locker room concrete floor complete  
 Concrete equipment pads completed at roof.  
 Spray on Fireproofing complete at basement ceiling – 1<sup>st</sup> level started week of 4/6, 100% complete  
 Plumbing piping ongoing at basement locker rooms – 90% complete  
 Interior masonry – started at level 1 on 4/13/09. Basement level to start 4/21/09  
 Roof parapet framing ongoing– 80%  
 Permanent roof insulation installation – scheduled to start late April  
 Removal of temporary winter protection – nearing completion  
 Elevator – installation to start early May

### Academic (C) / Cafeteria (C):

Concrete floors – complete  
 Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- 99% complete. Level 3 -98% complete, Level 2 – 96% complete, Level 1 -80% complete.  
 Exterior framing, sheathing – ongoing – 98% complete / Exterior flashings and waterproof barrier ongoing – 68% complete.  
 Window delivery – starting 4/27/09 +/-  
 Interior masonry partitions – ongoing – 98% complete  
 Exterior Masonry – Brick work started week of 2/2/09 – ongoing – 35% complete – brickwork is complete at south side & majority of east side of Area C with current activity at north side and above cafeteria area. Work progressing with two crews toward auditorium/theater.  
 Winter weather protection and temporary heating – removal nearly completed.  
 Permanent roof insulation – 100% of main complete. Rooftop Mech room – roofing installed week of 3/16/09  
 Delivery and installation of roof top HVAC Units – Area C units were delivered and set on roof – week of 3/16/09 Gas boilers set in roof mechanical room – week of 3/30. Misc pumps, panel boards, transformers delivered week of 4/13/09.

### Theater (D) –

Perimeter concrete foundations and structural steel - complete  
 Miscellaneous concrete Control room, stage and orchestra pit walls ongoing- 90%  
 Concrete ramp and floor preparation - started  
 Underground piping work – ongoing - 85%complete.-  
 Concrete floor at small theater - complete  
 Fireproofing paint @ structural steel– started – 15% complete  
 HVAC equipment (chiller) set in place - week of 4/6  
 Exterior Masonry – started 4/13.
