



Newton North High School


Project Areas by function / Current Construction Activity – 4/24/09

Pool/Small gym (B) –

Concrete foundations - complete
 Structural Steel erection – substantially complete – topping off ceremony held 12/12/08.
 Metal decking – 100% complete
 Temporary weather protection and temporary heating – removal completed -
 Concrete floor - level 1 and 2 complete
 Plumbing roof drainage piping – ongoing – 70% complete
 Swimming pool filter equipment – delivered 4/22/09
 Underground plumbing – started 4/17/09
 Fireproof paint at structural steel – ongoing- 25% complete

Academic (C)

Concrete floors: All levels - complete.
 Interior spray on fireproofing – level 2 & 3 – completed. Underside of roof fireproofing – 100% complete. Ground level – 80% complete.
 Underground piping/utilities below level 1 are complete
 Rough Mechanical/plumbing/ ductwork/electrical installation- Level 4 – 50% complete, Level 3 – 70% complete, Level 2 – 50% complete, Level 1 – 25 % complete.
 Interior Masonry - level's 2 and 3 – 98% complete. Ground level 95% complete
 Exterior framing, sheathing – 99% complete – exterior waterproofing ongoing.
 Permanent Roof Insulation work – 100% complete.
 Stair #5 installation completed.
 Winter weather protection and temporary heating removal – complete

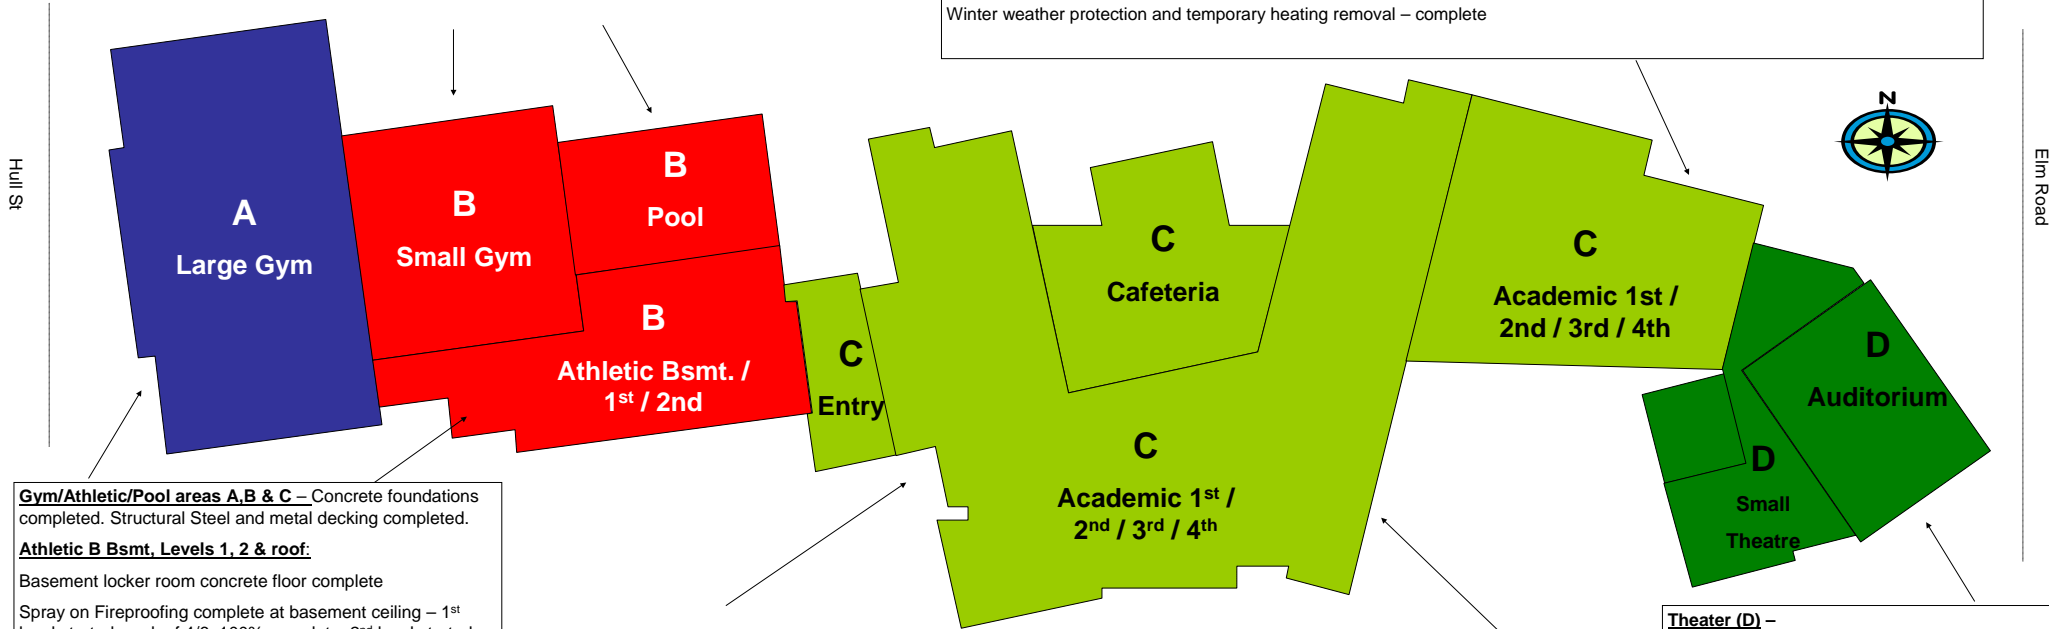

Gym/Athletic/Pool areas A,B & C – Concrete foundations completed. Structural Steel and metal decking completed.

Athletic B Bsmt, Levels 1, 2 & roof:

Basement locker room concrete floor complete
 Spray on Fireproofing complete at basement ceiling – 1st level started week of 4/6, 100% complete, 2nd level started
 Plumbing piping ongoing at basement locker rooms – 100% complete
 Interior masonry – started at level 1 on 4/13/09. Basement started 4/21/09
 Roof parapet framing ongoing– 90%
 Wall framing and sheathing started – 30%
 Permanent roof insulation installation – scheduled to start 5/18/09
 Removal of temporary winter protection – nearing completion
 Elevator – installation to start early May

Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- 99% complete. Level 3 -98% complete, Level 2 – 96% complete, Level 1 -85% complete.
 Exterior framing, sheathing – ongoing – 98% complete / Exterior flashings and waterproof barrier ongoing – 80% complete.
 Interior metal stud framing – 90% complete. 3rd floor ready for drywall installation in 1 week +/-.
 Window delivery – 1st delivery received 4/21/09, install to start
 Interior masonry partitions – ongoing – 98% complete
 Exterior Masonry – Brick work started week of 2/2/09 – ongoing – 35% complete – brickwork is complete at south side & majority of east side of Area C with current activity at north side and above cafeteria area. Work progressing with two crews toward auditorium/theater.
 Winter weather protection and temporary heating removal - complete
 Permanent roof insulation – 100% of main complete. Rooftop Mech room – roofing installed week of 3/16/09
 Delivery and installation of roof top HVAC Units – Area C units were delivered and set on roof – week of 3/16/09 Gas boilers set in roof mechanical room – week of 3/30. Misc pumps, panel boards, transformers delivered week of 4/13/09.

Theater (D) –

Perimeter concrete foundations and structural steel - complete
 Miscellaneous concrete Control room, stage and orchestra pit walls complete 100%. Second floor – concrete floor – partial installation scheduled week of 4/27/09
 Underground piping work - 100%complete.
 Concrete floor at small theater - complete
 Fireproofing paint @ structural steel– ongoing– 60% complete
 HVAC equipment (chiller) set in place - week of 4/6, piping ongoing
 Masonry - Exterior – started 4/13 – ongoing – 20% complete. Masonry – Interior- ongoing – 10% complete
