

Newton North High School


Project Areas by function / Current Construction Activity – 5/08/09

Pool/Small gym (B) –

Concrete foundations and steel erection is complete - complete
 Concrete floors - level 1 and 2 complete
 Plumbing roof drainage piping – ongoing – 85% complete
 Underground plumbing – ongoing – 10% complete
 Pool HVAC Dehumidification Equipment – delivered and set in place
 Fireproof paint at structural steel – ongoing- 50% complete
 Exterior Masonry – starting 5/11/09 +/-
 Permanent roof to start 6/1/09 +/-

Academic (C)

Concrete floors: All levels - complete.
 Interior spray on fireproofing – level 2 & 3 & 4 – completed. Ground level – 80% complete – completion will occur subsequent to low roofing installation
 Rough Mechanical/plumbing/ ductwork/electrical installation- Level 4 – 85% complete, Level 3 – 80% complete, Level 2 – 70% complete, Level 1 – 25 % complete.
 Interior metal studs / drywall – will start 5/11/09.
 Interior Masonry – level 4 – 98% complete, level's 2 and 3 – 98% complete. Ground level 95% complete
 Exterior Masonry – ongoing - 50% complete
 Exterior framing, sheathing – 99% complete – exterior waterproofing ongoing – 75% complete
 Permanent Roof Insulation work (except at low roof) – 100% complete.
 Stair #5 installation completed-

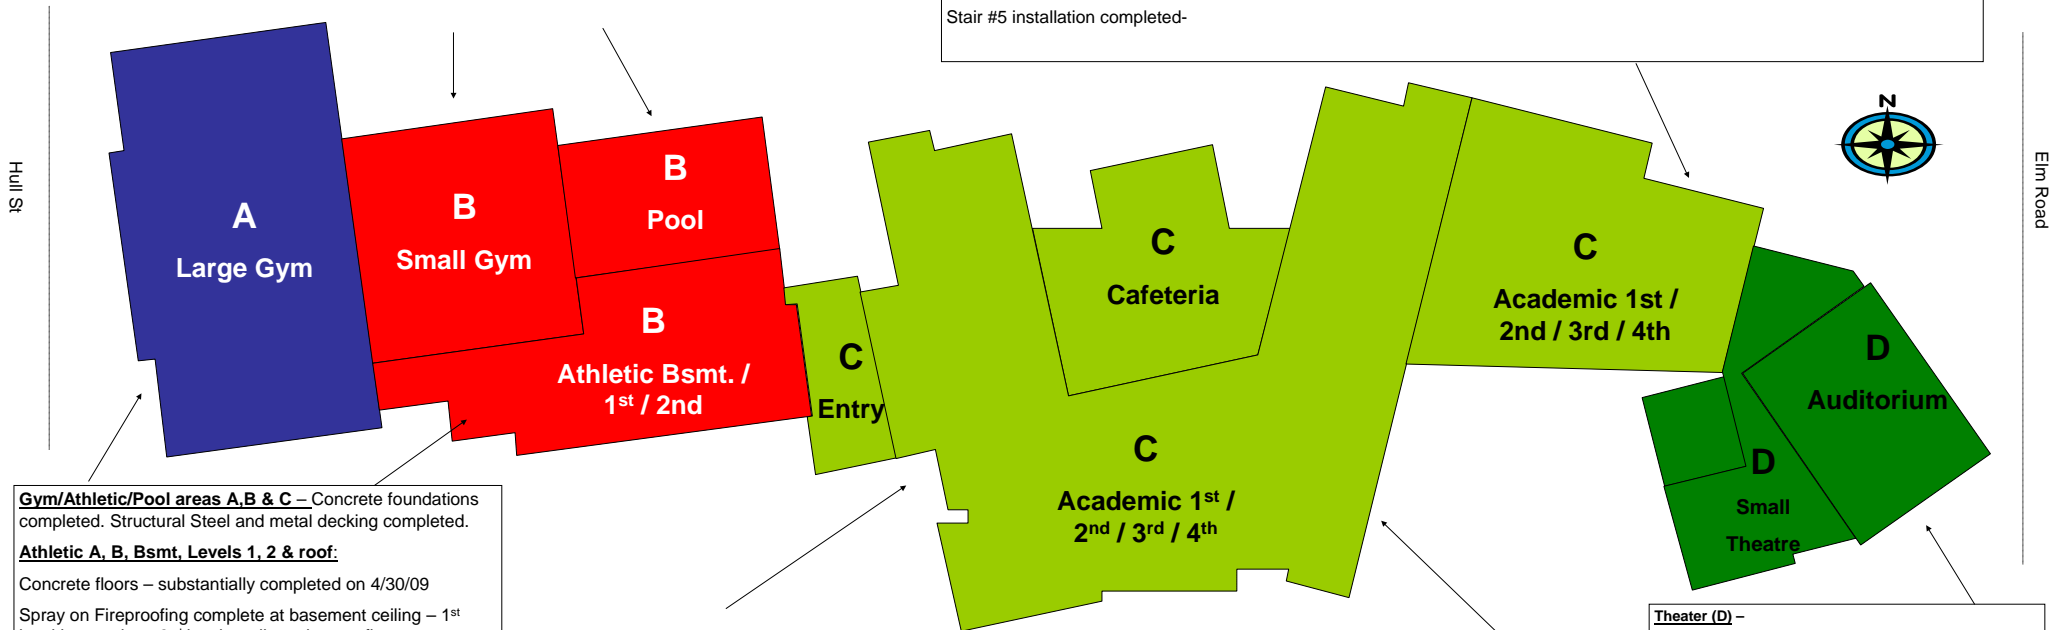

Gym/Athletic/Pool areas A,B & C – Concrete foundations completed. Structural Steel and metal decking completed.

Athletic A, B, Bsmt, Levels 1, 2 & roof:

Concrete floors – substantially completed on 4/30/09
 Spray on Fireproofing complete at basement ceiling – 1st level is complete, 2nd level predicated on roofing
 Plumbing rough in piping complete at basement locker rooms – 100% complete
 Interior masonry – level 1- ongoing- 85 % complete, basement – ongoing – 45%. Level 2- will start on 5/16/09 +/-.
 Roof parapet framing ongoing– 90%
 Wall framing and sheathing ongoing – 85%
 Stair #1 – started – 50% complete
 Permanent roof insulation installation – Athletic “B” roof – defered to 5/11/09 due to weather, Athletic A – 5/18/09 (permanent insulation/roofing)
 Elevator A – start installation week of 5/11/09

Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- 99% complete. Level 3-98% complete, Level 2 – 98% complete, Level 1 -88% complete.
 Exterior framing, sheathing – ongoing – 98% complete / Exterior flashings and waterproof barrier ongoing – 95% complete.
 Interior metal stud framing – 90% complete. 3rd floor ready for drywall installation - start contingent on window installation
 Window delivery – ongoing – installation started 5/4/09.
 Interior masonry partitions – ongoing – 98% complete.
 Exterior Masonry – Brick work started week of 2/2/09 – ongoing – 90% complete
 Permanent roof insulation / Temporary roof – 100% of main complete.
 Delivery and installation of roof top HVAC Units – Area C is complete.
 Elevator B – ongoing – elevator platform is running
 Removal of temporary stair tower – scheduled for 6/18/09.

Theater (D) –

Perimeter concrete foundations and structural steel and small theater floor concrete - complete
 Miscellaneous concrete Control room, stage and orchestra pit walls complete 100%. Second floor – concrete & stage roof – placed 4/27/09 – orchestra pit floor slab scheduled for 5/8/09, stage slab floor scheduled for 5/15/09.
 Exterior Masonry at large theater stage perimeter – starting week of 5/11/09.
 Underground piping work - complete.
 Permanent roofing @ small theater – start 5/14/09 +/-
 Fireproofing paint @ structural steel– ongoing– 75% complete – no change due to weather
 HVAC equipment (chiller) set in place - week of 4/6, piping ongoing
 Masonry - Exterior – started 4/13 – ongoing – 25% complete. Masonry – Interior- ongoing – 20% complete
 Rooftop HVAC Units – will be set in place 5/20 +/-
