



Newton North High School

Project Areas by function / Current Construction Activity – 5/29/09

Site work – General Items


Granite curb at North lot – ongoing
 Site drainage piping at Ceremonial Drive
 Site electrical – northwest parking area
 Stadium retaining wall excavation to start 5/29/09

Pool/Small gym (B) –

Concrete foundations and steel erection is complete
 Concrete floors - level 1 and 2 complete
 Plumbing roof drainage piping – ongoing – 95% complete
 Underground plumbing – ongoing – 20% complete
 Fireproof paint at structural steel – ongoing- 90% complete
 Exterior Masonry – ongoing – 55%
 Permanent roof to start 6/1/09 +/-

Academic (C)

Concrete floors: All levels - complete.
 Interior spray on fireproofing – level 2 & 3 & 4 – completed. Ground level – 80% complete – completion will occur subsequent to low roofing installation
 Rough Mechanical/plumbing/ ductwork/electrical installation- Level 4 – 95% complete, Level 3 – 95% complete, Level 2 – 83% complete, Level 1 – 30 % complete.
 Interior metal studs – level 2 and 3 – complete. Level 4 – 85%
 Interior Masonry – level 4 – 98% complete, level's 2 and 3 – 99% complete. Ground level 95% complete
 Exterior Masonry – ongoing - 75% complete
 Exterior framing, sheathing – 99% complete – exterior waterproofing ongoing – 90% complete
 Permanent Roof Insulation work (except at low roof) – 100% complete.
 Stair #5 - complete

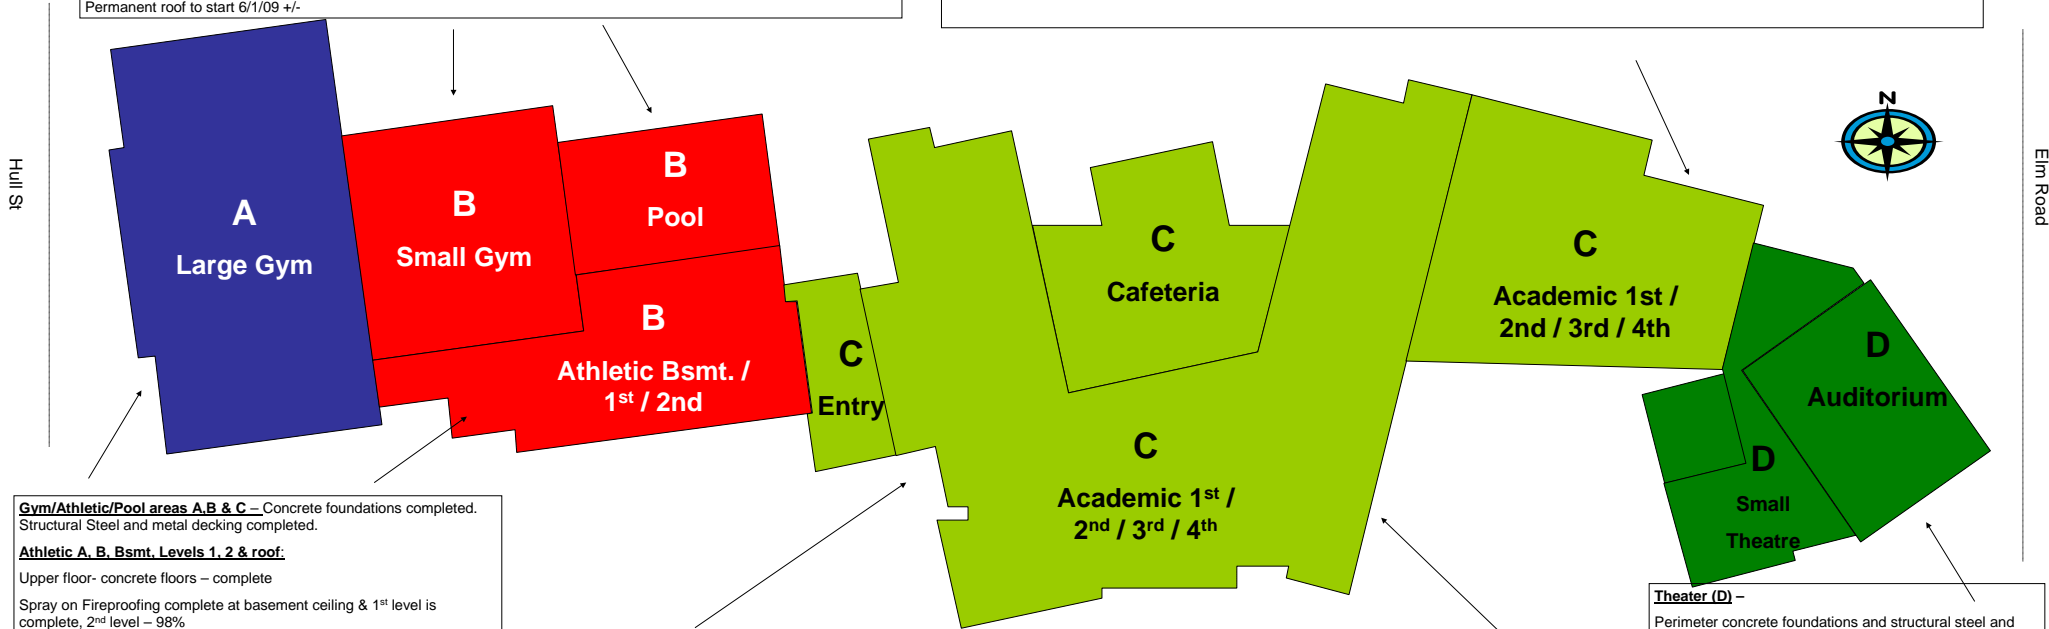

Gym/Athletic/Pool areas A,B & C – Concrete foundations completed. Structural Steel and metal decking completed.

Athletic A, B, Bsmt. Levels 1, 2 & roof:

Upper floor- concrete floors – complete
 Spray on Fireproofing complete at basement ceiling & 1st level is complete, 2nd level – 98%
 Plumbing rough in piping complete at basement locker rooms – 100% complete
 Interior masonry – level 1- ongoing- 88 % complete, basement – ongoing – 80%. Level 2 – started – 15% complete.
 Roof parapet framing ongoing– 95%
 Wall framing and sheathing ongoing – 95%
 Window flashings/Exterior vapor barrier – ongoing – 15%
 Stair #1 – started – 65% complete
 Permanent roof insulation installation – Athletic “B” roof – completed week of 5/11/09, Athletic A – material delivered – install to start 6/1/09.
 Elevator A – ongoing – constructing platform
 Mechanical/Electrical/Plumbing – Overhead piping started at basement level.

Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- 99% complete. Level 3-98% complete, Level 2 – 98% complete, Level 1 -90% complete. Continuance of level 1 contingent on cafeteria roof installation.
 Exterior framing, sheathing – ongoing – 98% complete / Exterior flashings and waterproof barrier ongoing – 98% complete.
 Interior metal stud framing – 100% complete. 3rd floor ready for drywall installation – drywall started 5/28/09.
 Window delivery/installing – ongoing – 25%
 Curtain Wall – starting 6/1/09
 Interior masonry partitions – ongoing – 98% complete.
 Exterior Masonry – Brick work started week of 2/2/09 – ongoing – 95% complete
 Permanent roof insulation / Temporary roof – 100% of main complete – permanent roofing to be installed mid June 2009.
 Culinary Arts – walk in coolers being delivered week of 6/1/09 +/- . Kitchen exhaust hoods installed week of 5/18/09
 Elevator B – ongoing – elevator platform complete – elevator entrances – complete – cab assembly started.
 Stair 4 - Steel and landing metal deck completed 5/26 – Stair installation started

Theater (D) –

Perimeter concrete foundations and structural steel and small theater floor concrete - complete
 Miscellaneous concrete. Control room, stage and orchestra pit walls complete 100%. Second floor concrete complete – orchestra pit floor slab complete, stage floor concrete to be installed week of 6/1/09
 Exterior Masonry at large theater perimeter – started. Exterior masonry is near complete at small theater
 Interior Masonry at small theater 90% complete
 Underground piping work - complete.
 Permanent roofing @ small theater – temporary roof installed
 Fireproofing paint @ structural steel– ongoing– 100% complete. Spray on Fireproofing to be completed subsequent to roofing
 HVAC equipment (chiller) is in place. Chiller pumps delivered week of 5/25/09.
 Rooftop HVAC Units –set in place 5/29/09
