

Newton North High School

Project Areas by function / Current Construction Activity – 6/06/09

Site work – General Items


Screening / distributing topsoil
 Site drainage and telecommunication duct bank piping at Ceremonial Drive ongoing
 Stadium retaining wall – concrete footings – started 6/1/09
 Miscellaneous site grading / site utility work

Pool/Small gym (B) –

Concrete foundations and steel erection is complete
 Concrete floors - level 1 and 2 complete
 Plumbing roof drainage piping – ongoing – 95% complete
 Underground plumbing – ongoing – 20% complete
 Fireproof paint at structural steel – ongoing- 90% complete
 Exterior Masonry (SMU) – ongoing – 85 %
 Permanent roof to start 6/9/09 +/-

Academic (C)

Concrete floors: All levels - complete.
 Interior spray on fireproofing – level 2 & 3 & 4 – completed. Ground level – 80% complete – completion will occur subsequent to low roofing installation
 Rough Mechanical/plumbing/ ductwork/electrical installation- Level 4 – 95% complete, Level 3 – 95% complete, Level 2 – 90% complete, Level 1 – 35 % complete.
 Interior metal studs – level 2 and 3 – complete. Level 4 – 100%
 Interior Masonry – level 4 – 98% complete, level's 2 and 3 – 99% complete. Ground level 95% complete
 Exterior Masonry – ongoing - 85% complete
 Exterior framing, sheathing – 99% complete – exterior waterproofing ongoing – 90% complete
 Permanent Roof Insulation work (except at low roof) – 100% complete.
 Stair #5 - complete

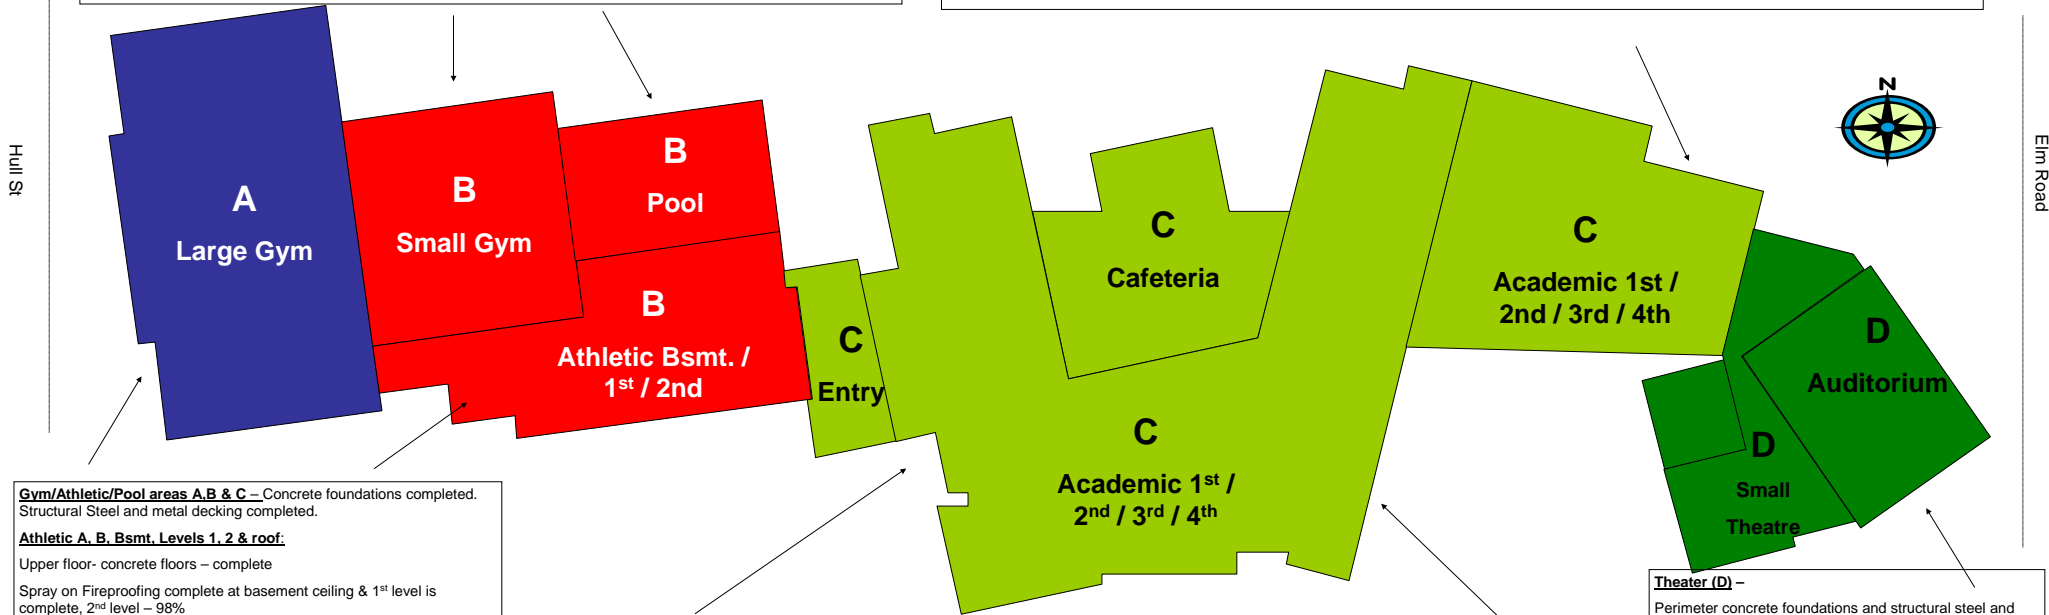

Gym/Athletic/Pool areas A,B & C – Concrete foundations completed. Structural Steel and metal decking completed.

Athletic A, B, Bsmt. Levels 1, 2 & roof:

Upper floor- concrete floors – complete
 Spray on Fireproofing complete at basement ceiling & 1st level is complete, 2nd level – 98%
 Plumbing rough in piping complete at basement locker rooms – 100% complete
 Interior masonry – level 1- ongoing- 92 % complete, basement – ongoing – 90%. Level 2 – started – 30% complete. Masonry started in large gym
 Roof parapet framing ongoing– 98%
 Wall framing and sheathing ongoing – 95%
 Window flashings/Exterior vapor barrier – ongoing – 20%
 Stair #1 – started – 70% complete
 Permanent roof insulation installation – Athletic “B” roof – completed week of 5/11/09, Athletic A – ongoing 50%.
 Elevator A – ongoing – platform complete – elevator cab started
 Mechanical/Electrical/Plumbing – Overhead piping at basement level – ongoing – 40%

Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- 99% complete. Level 3-98% complete, Level 2 – 98% complete, Level 1 -90% complete. Continuance of level 1 contingent on cafeteria roof installation.
 Exterior framing, sheathing – ongoing – 98% complete / Exterior flashings and waterproof barrier ongoing – 98% complete.
 Drywall – level 3 –ongoing, 30% complete. Drywall to start on level 4 6/15/09 +/-.
 Window delivery/installing – ongoing – 50%
 Curtain Wall – started at stair 2 – 6/2/09
 Interior masonry partitions – ongoing – 98% complete.
 Exterior Masonry – Brick work started week of 2/2/09 – ongoing – 99% complete
 Permanent roof insulation / Temporary roof – 100% of main complete – permanent roofing to be installed mid June 2009.
 Culinary Arts – Kitchen exhaust hoods installed week of 5/18/09. Walk in cooler at culinary arts installed 6/2/09
 Elevator B – ongoing – elevator platform complete – elevator entrances – complete – cab assembly ongoing
 Stair 4 - Steel and landing metal deck completed 5/26 – Stair installation ongoing and will complete 6/11/09.

Theater (D) –

Perimeter concrete foundations and structural steel and small theater floor concrete - complete
 Miscellaneous concrete. Control room, stage and orchestra pit walls complete 100%. Second floor concrete complete – orchestra pit floor slab complete, stage floor concrete floor completed on 5/29/09.
 Exterior Masonry at large theater perimeter – started. Exterior masonry is near complete at small theater
 Water proofing started at small theater 6/3/09.
 Interior Masonry at small theater 90% complete
 Permanent roofing @ small theater – temporary roof installed
 Fireproofing paint @ structural steel– ongoing– 100% complete. Spray on Fireproofing to be completed subsequent to roofing.
 HVAC equipment (chiller) is in place. Chiller pumps delivered week of 5/25/09, piping ongoing.
 Rooftop HVAC Units – set in place 5/29/09.
