



# Newton North High School

## Project Areas by function / Current Construction Activity – 01/08/10

### Site work – General Items

Football field/track – subbase preparation - completed, drainage – 99% / Bleacher installation – 99% - paving-complete  
 Perimeter sidewalks ongoing – 55%  
 Tennis court retaining wall- completed / Tennis Ct lighting bases – complete , Hull St concrete stairway - complete - final sub grade prep - substantially completed  
 Loading Dock footing and walls – complete, backfilling nearly complete – slab preparation ongoing  
 Grading and granite curb – Ceremonial Drive – ongoing – curb 95%, roadway grading 100% - paving completed 12/3/09.  
 NOTE – Exterior work to largely resume – Spring 2010

### Pool/Small gym (B) –


Concrete slabs – substantially complete (natatorium pool perimeter slab remaining)  
 Permanent roof –substantially complete – roof flashings –completed / perimeter roof edge copings 70%  
 Swimming pool gunite installation completed – backfill at pool perimeter 98% complete/ started pool water testing  
 Swimming pool perimeter slab – trench drain installation - 35%  
 Prime painting and 1<sup>st</sup> finish coat painting at small gym – walls and ceiling – completed.  
 Misc interior masonry work in pool shower area – 98% compl. / Plumbing piping for pool area showers/baths – 98% compl  
 Athletic Equip – basketball backboards, divider, scoreboards, public address system - completed - small gym – same work ongoing in lrg gym – all 95% complete  
 Wood Flooring delivered – large gym - installation to start January 2010

### Academic (C)

Classroom casework installation – level 4 - complete, level 3 – complete, level 2 – 90%, level 1 – 55%  
 Locker installation – level 4 – 99% complete%, level 3 – 90%. Level 2 – 50%  
 Rough Mechanical/plumbing/ ductwork/electrical installation- Level 4 – 100% complete, Level 3 – 99% complete, Level 2 – 98% complete, Level 1 – 98 % complete. MEP above ceiling punch lists being completed ahead of ceiling time installations  
 Interior metal studs – level 2 – 100% complete, level's 3 and 4 – complete. Level 2 complete, Lev 1 - 80%  
 Interior drywall – started 6/26/09 @ Lev 3 – complete, Lev 4– complete, Lev 2 - complete, Lev 1- 90%  
 Prime Painting – Level 3 – 100%, Level 4 – 100%, Level 2 – 100%, Level 1 – 99% - Finish painting ongoing.  
 Exterior Masonry (Brick) - complete / exterior metal panels – 99% complete  
 Permanent Roof Insulation work (except at low roof) – completed. Lower roof membrane complete  
 Ceiling grid installation - 95% overall  
 Window installation – ongoing - 100% complete / Curtain wall framing & glazing – 98%  
 Operable partitions – framing and track installed  
 Overhead doors (exterior) – completed / Interior doors/frames and hardware- ongoing  
 Resinous flooring – 70% overall

Hull St

Elm Road

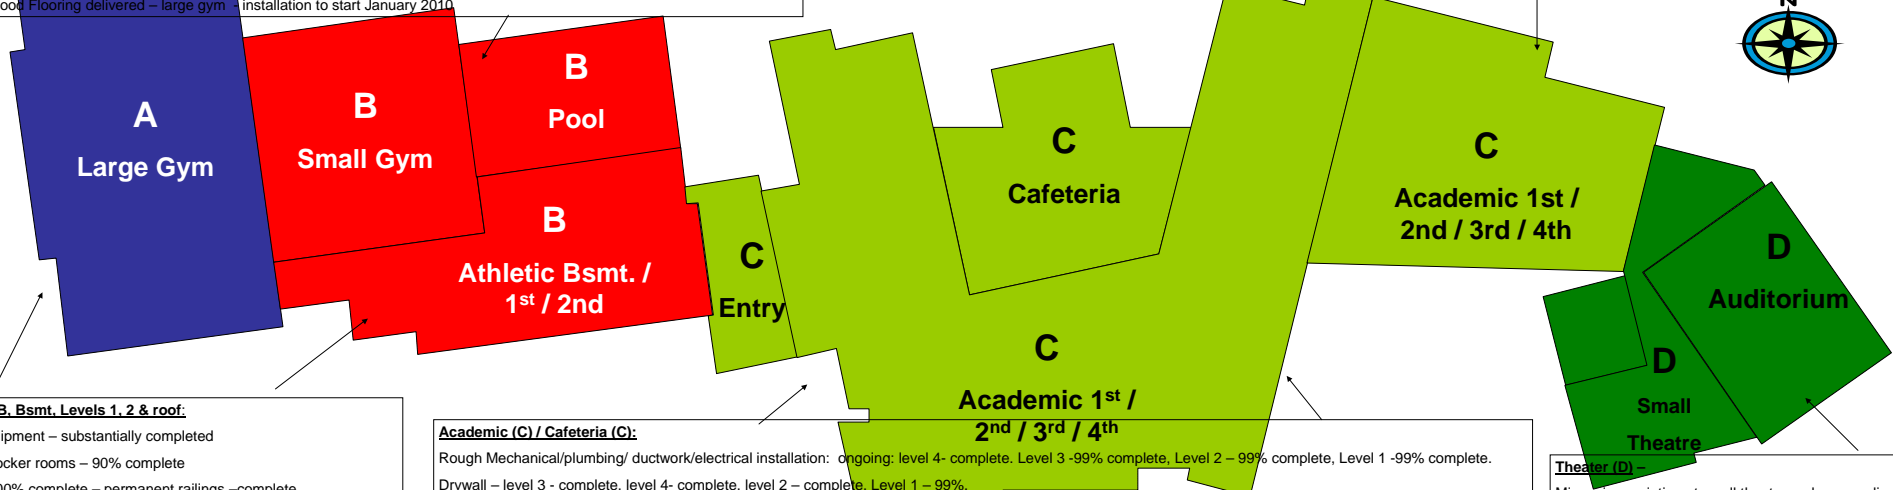

### Athletic A, B, Bsmt, Levels 1, 2 & roof:

Athletic equipment – substantially completed  
 Lockers at locker rooms – 90% complete  
 Stair #1 – 100% complete – permanent railings –complete  
 Mechanical/Electrical/Plumbing – Overhead piping at basement level - substantially complete – Overhead piping large gym – 98% complete  
 Roof Top HVAC units – set in place on 6/22 – piping work 95% complete  
 Interior Metal Stud framing – complete / drywall 88% complete  
 Natatorium seating area – concrete and masonry work completed  
 Misc drywall @ Child care - complete  
 Mechanical overhead piping at large gym – 95% complete.  
 Kalwall windows – completed 12/8/09  
 Curtain wall – ongoing – 90% complete  
 Ceiling grid – basements – ongoing 90%, 1<sup>st</sup> floor – 70%  
 Low permanent roof at elevator – completed.  
 Elevator - final adjustments – ongoing for elevator inspection in mid Jan  
 Resinous flooring – ongoing – 50%  
 Wood flooring – delivered – install to start 1to2 wks.

### Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- complete, Level 3 -99% complete, Level 2 – 99% complete, Level 1 -99% complete.  
 Drywall – level 3 - complete, level 4- complete, level 2 – complete, Level 1 – 99%.  
 Prime Painting – level 3 – complete, level 4– complete, level 2 – complete, level 1 -97% complete. 1<sup>st</sup> finish coat started @ Level 3 and 4 -complete – 1<sup>st</sup> coat finish painting level 2 -98% – misc prime painting ongoing level 1-90%  
 Window /installation– ongoing – 99% / Curtain Wall installation - ongoing – 95% - Cafeteria large curtain wall glazing – 98%  
 Main st soffits and drywall – ongoing – 95%  
 Permanent roofing roof – main roof complete. Cafeteria permanent roof – complete. Perimeter roof copings – 60%  
 Elevator B and C -- elevator inspection upcoming - temporary inspection certificate completed at elevator B.  
 Exterior metal panel work – ongoing- 90%  
 Acoustic ceiling grid – level 3 – 100%, level 4 – 100%, Level 2 – 100% , Level 1 – 90% - install ceiling tile – level 4 – complete, Level 3 – 98%, level 2 – 60%, lev 1 - 20%  
 Electrical devices / trimout -ceilings & light fixtures – level 3 – 90%, level 4 – 95%, level 2 – 85%, Lvl 1- 30%  
 Science lab/classroom casework – Level 4 – 98% , Level 3 – 95% complete – deliveries ongoing. Mechanical/Plumbing/Electrical hookups following installation, level 2 – 80%, level 1 – 40%.  
 Resinous Flooring – level 4 – complete, level 3 – 90% - level 2 – 60% - plumbing fixtures ongoing – level 4, 3, and 2 - 85%  
 Quarry Tile flooring preparation at Kitchen complete on 12/10. / VCT material deliveries started 10/30/09 – QT at culinary arts – ongoing -80% complete.  
 Vinyl flooring – level 4- 90%, level 3 – 65%  
 Locker installation – Level 4 – 99%, level 3 – 95%, Lvl 2 – 75%, Lvl1 - 30%  
 Wood door / hardware installation – Lvl 4 – 80%, level 3 started / Marker/tack board started – all areas – 90% / coiling doors all areas – 99%

### Theater (D) –

Misc prime painting at small theater and surrounding areas - completed  
 (temporary work platform has been removed – overhead MEP at theater- complete. overhead millwork –completed.  
 Interior Masonry at small theater 100% complete, large theater 100% complete – ext brick is 100% complete.  
 Fireproofing paint @ structural steel completed. Spray on Fireproofing –complete – misc patching ongoing  
 HVAC equipment (chiller) is in place, piping at pump room – 98% complete – distribution piping – 98%.  
 Theater lighting & controls rough ins – ongoing – 85%  
 Overhead steel catwalk /spiral stairs work ongoing –98%  
 Interior misc metal railings - started  
 Curtain wall @ Theater entry – 98% complete  
 Theater rigging - 95%  
 Small theater drywall – 85% complete  
 Wheelchair lifts – start Jan/2010  
 Theater interior finishes – starting in next two/three wks
