



Newton North High School

Project Areas by function / Current Construction Activity – 03/26/10

Site work – General Items


Football field/track – subbase preparation - completed, drainage – 99% / Bleacher installation – 99% - paving-complete
 Perimeter sidewalks ongoing – 68% - completed main entry and theater entrance plazas
 Tennis court retaining wall- completed / Tennis Ct lighting bases – complete , Hull St concrete stairway - complete - final sub grade prep - substantially completed
 Loading Dock – substantially completed
 Grading and granite curb – Ceremonial Drive – ongoing – curb 95%, roadway grading 100% - paving completed 12/3/09.
 Project temporary offices have been relocated – office trailers removed – underground utility and grading work scheduled late March

Pool/Small gym (B) –

Perimeter roof flashings/ roof edge copings 95%
 Natatorium – pool interior waterproofing completed – pool being water tested – tile work to follow
 Elevated pool seating area – seating installation started
 Pool Locker room finishes (tile)- 96% complete
 Small Gym - Wood flooring installation – 60%
 Athletic Equip – basketball backboards, divider, scoreboards, public address system - completed at both gyms

Academic (C)

Classroom casework installation – level 4 - complete, level 3 – complete, level 2 – complete, level 1 – 98%
 Locker installation – level 4 – 100% complete%, level 3 – 100%. Level 2 – 100%
 Rough Mechanical/plumbing/ ductwork/electrical installations- all rough in activities completed – air balancing and started. System and equipment commissioning ongoing
 Painting – Level 3 – 100%, Level 4 – 100%, Level 2 – 100%, Level 1 – 99% - Finish painting ongoing and nearing completion in all areas of Area C
 Misc floor finishes – carpet / VCT substantially level 1, levels 2, 3, 4 substantially complete
 Roofing - perimeter copings ongoing
 Ceiling grid installation - 99% overall / ceiling tile - 96% complete
 Window installation – 100% complete / Curtain wall framing & glazing – 100%. Entry doors and hardware nearly completed
 Overhead doors (exterior) – completed / Interior doors/frames and hardware- nearly complete
 Interior glass and glazing – 94% complete
 Resinous flooring – complete
 Resilient flooring/vinyl sheet goods – 90% overall complete
 Punch list activity in process at levels 4, 3 and 2.

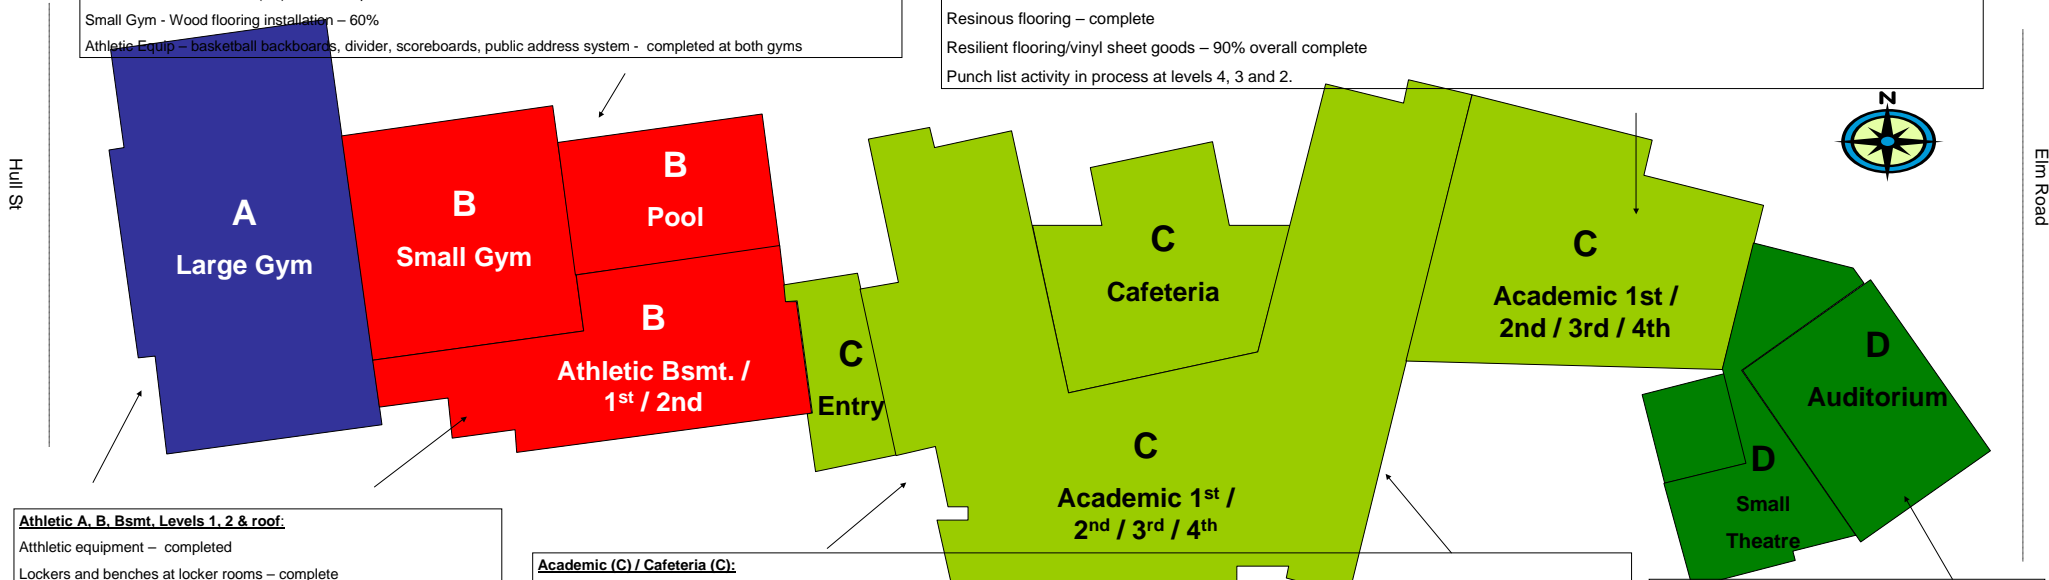

Athletic A, B, Bsmt, Levels 1, 2 & roof:

Athletic equipment – completed
 Lockers and benches at locker rooms – complete
 Large gym – synthetic flooring 90% complete. Game/ track lines – late March
 Mechanical/Electrical/Plumbing – Overhead piping at basement level - substantially complete – Overhead piping large gym – 100% complete
 Roof Top HVAC units – set in place on 6/22 – piping work 100% complete
 Mechanical overhead piping at large gym – 100% complete.
 Kalwall windows – complete
 Curtain wall – ongoing – 100% complete, aluminum entrances near complete.
 Ceiling grid – basements – ongoing 99%, 1st floor – 99%, 2nd floor – 98%
 Low permanent roof at elevator – completed.
 Elevator - temp use certificate received – elevator being utilized for material distribution –Final inspection expected mid April
 Resinous flooring – ongoing – 100%
 Ceramic Tile –basement – 94%
 Synthetic flooring at dance room – completed.
 Photovoltaic installation – ongoing and continuing weather dependant

Academic (C) / Cafeteria (C):

Rough Mechanical/plumbing/ ductwork/electrical installation: ongoing: level 4- complete, Level 3 –100% complete, Level 2 – 100% complete, Level 1 -99% complete.
 Prime Painting – 100% complete. Final coat painting – ongoing all areas –99% complete
 Window /installation– complete / Curtain Wall installation - complete. Aluminum entry doors and hardware nearing completion
 Permanent roofing roof – main roof complete. Cafeteria permanent roof – complete. Perimeter roof copings – 92%
 Exterior metal panel work – ongoing- 98%
 Acoustic ceiling grid – level 3 – 100%, level 4 – 100%, Level 2 – 100% , Level 1 – 99% - install ceiling tile – level 4 – complete, Level 3 – 100%, level 2 – 98%, lev 1 - 96%
 Electrical devices / trimout -ceilings & light fixtures – level 3 – 99%, level 4 – 98%, level 2 – 98%, Lvl 1- 95%
 Science lab/classroom casework – Level 4 – 100% , Level 3 – 100% complete, level 2- 93%, Level 1 – 90%. Mechanical/Plumbing/Electrical hookups following installation.
 Resinous Flooring – level 4 – complete, level 3 – 100% -level 2 – 100%, level 1 – 100% - plumbing fixtures ongoing – level 4, 3, and 2, and 1 - 96%
 Food Service equipment deliveries – completed – utility hookups at kitchen and culinary arts – 70%
 Vinyl flooring – level 4- 100%, level 3 – 98%, level 2 – 96%, level 1 – 90%
 Locker installation – Level 4 – complete, level 3 – 100%, Lvl 2 – 99%, Lvl1 - 95%
 Wood door / hardware installation – Lvl 4 – 100%, level 3 – 100%, lev 2 – 99%, lvl 1 – 96% / Marker/tack board started – all areas – 99% / coiling doors all areas – completed
 Carpet installation @ library – 100% complete, carpet vinyl base to be completed end of March
 Punch list activity in process at levels 4,3 and 2.

Theater (D) –

Finish painting nearing substantial completion
 Acoustical wall panel frames -installed
 Acoustical wall panels at theater - started
 HVAC equipment (chiller) is in place, piping at pump room – 99% complete – distribution piping – 99%.
 Theater lighting & controls rough ins – ongoing – 99%
 Overhead steel catwalk /spiral stairs work – complete
 HP lifts – 100% installed
 Theater rigging - substantially complete
 Theater seating – 90% complete
 Wood flooring @ small theater – complete
 Main stage /millwork –ongoing – 90% complete
 Carpet at theater – 60% complete
 Stage Flooring – ongoing, 70% complete
 Performance theater – tiered platforms – 80% complete
