

Newton North High School

Project Areas by function / Current Construction Activity 04/09/10

Site work – General Items


Football field/track – subbase preparation and fine grading completed – synthetic turf deliveries expected to start 4/9
 Perimeter sidewalks ongoing – 64% - completed main entry and theater entrance plazas, west side of athletic areas ongoing
 Tennis Ct area: lighting bases – complete , Hull St concrete stairway - railings completed, permanent fence posts started, connecting sidewalks ongoing, permanent light poles substantially complete.
 Loading Dock – Concrete work completed.
 Grading and granite curb – Ceremonial Drive – ongoing – curb 95%. Granite curbing ongoing outside theater area.
 Project temporary offices have been relocated – office trailers removed – site grading ongoing this area
 Landscaping to start week of 4/12/10

Pool/Small gym (B) –

Perimeter roof flashings/ roof edge copings 100%
 Natatorium – pool tiling has started, elevated spectator seating completed.
 Pool Locker room finishes (tile, resinous flooring)- 98% complete
 Small Gym - Wood flooring installation – 60%
 Athletic Equip – basketball backboards, divider, scoreboards, public address system - completed at both gyms

Academic (C)

Punch list activities - all floors
 Classroom casework installation – substantially complete
 Locker installation – substantially complete
 Rough Mechanical/plumbing/ ductwork/electrical installations- all rough in activities completed – air balancing ongoing. System and equipment commissioning ongoing
 Painting – Level 4,3,2 complete, Level 1 – 99% - Finish painting ongoing and nearing completion in all areas of Area C
 Misc floor finishes – carpet / VCT substantially complete. Rubber treads and risers at stairways ongoing
 Roofing - perimeter copings substantially complete
 Ceiling grid and tile installation – substantially complete.
 Window installation – 100% complete / Curtain wall framing & glazing – 100%. Entry door hardware & security system trimout nearly completed
 Overhead doors (exterior) – completed / Interior doors/frames and hardware- nearly complete
 Interior glass and glazing – 99% complete
 Resinous flooring – complete
 Resilient flooring/vinyl sheet goods – 99% overall complete

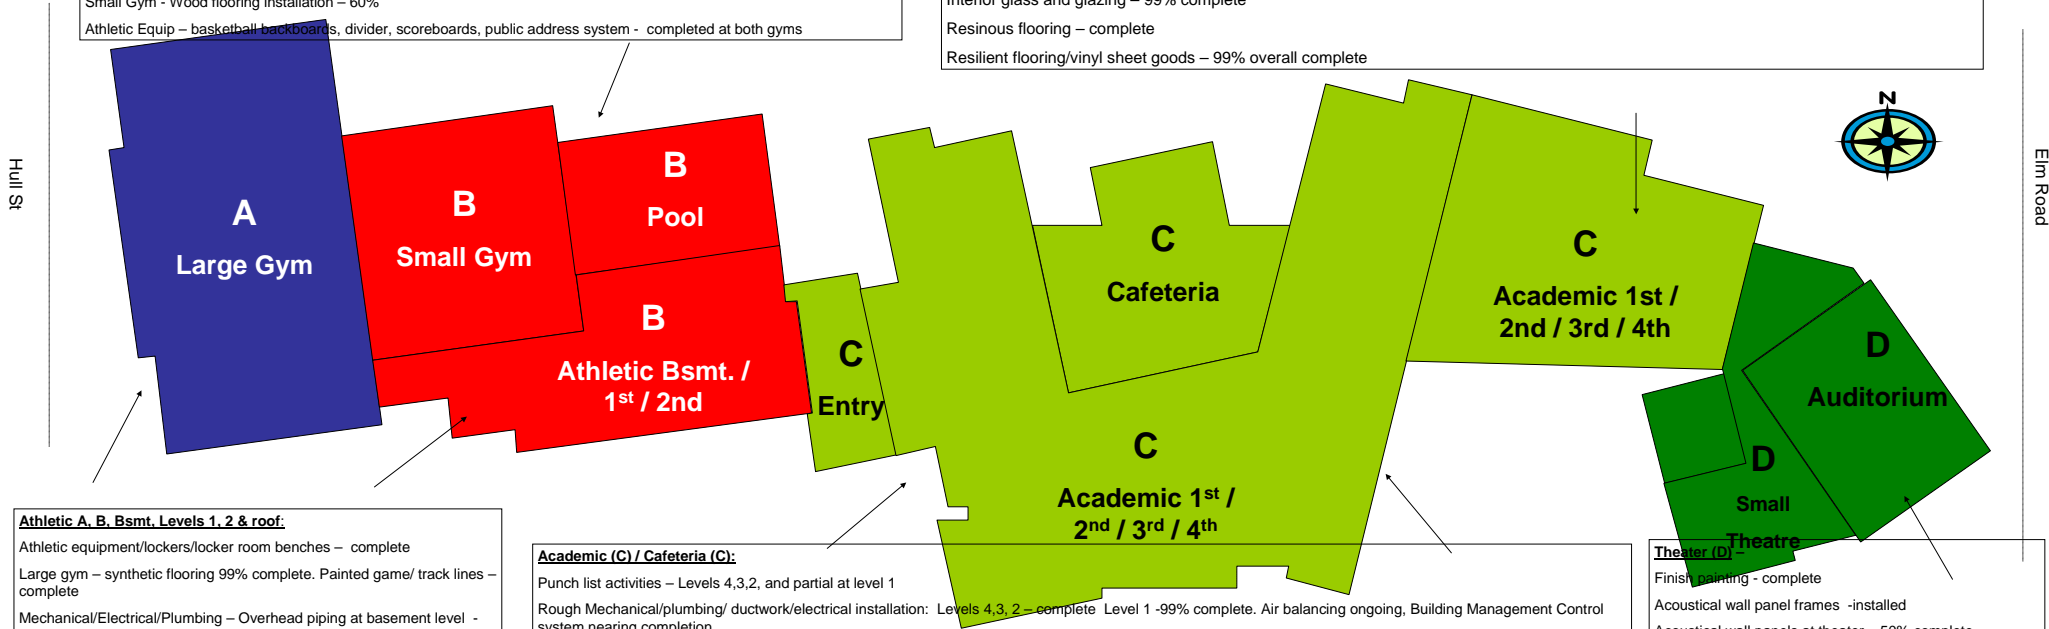

Athletic A, B, Bsmt, Levels 1, 2 & roof:

Athletic equipment/lockers/locker room benches – complete
 Large gym – synthetic flooring 99% complete. Painted game/ track lines – complete
 Mechanical/Electrical/Plumbing – Overhead piping at basement level - substantially complete – Overhead piping large gym – 100% complete
 Mechanical overhead piping at large gym – 100% complete.
 Kalwall windows – complete
 Curtain wall – ongoing – 100% complete, aluminum entrances near complete.
 Ceiling grid – basements – ongoing 99%, 1st floor – 99%, 2nd floor – 100%
 Low permanent roof at elevator roof copings – substantially completed.
 Elevator - temp use certificate received – elevator being utilized for material distribution –Final inspection expected mid April
 Ceramic Tile –basement – 99%
 Synthetic flooring at dance room – completed.
 Misc Mechanical/Electrical/Plumbing trim out – near complete
 Photovoltaic installation at roof – ongoing and continuing weather dependant – 75% complete

Academic (C) / Cafeteria (C):

Punch list activities – Levels 4,3,2, and partial at level 1
 Rough Mechanical/plumbing/ ductwork/electrical installation: Levels 4,3, 2 – complete Level 1 -99% complete. Air balancing ongoing, Building Management Control system nearing completion.
 Fire Alarm / Emergency Lighting inspections – near complete.
 Painting – 98% complete.
 Window /installation– complete / Curtain Wall installation - complete. Aluminum entry doors, hardware, and security trim out and devices nearing completion
 Permanent roofing – complete. Cafeteria permanent roof – complete. Perimeter roof copings – substantially complete %
 Exterior metal panel work – ongoing- 99%
 Acoustic ceiling grid and ceiling tile – substantially completed levels 4,3, and 2 – level 1 98%. –
 Electrical devices / trimout -ceilings & light fixtures – level 3 – 99%, level 4 – 99%, level 2 – 99%, Lvl 1- 97%
 Science lab/classroom casework – Level 4, 3 and 2 substantially complete, Level 1 – 98%. Mechanical/Plumbing/Electrical hookups following installation.
 Resinous Flooring – completed all areas
 Food Service equipment deliveries – completed – utility hookups at kitchen and culinary arts – 95%
 Vinyl flooring – Level 4, 3, 2 – substantially complete – level 1 98%
 Locker installation – complete
 Wood door / hardware installation – Levels 4, 3, 2 – substantially complete – level 1 – 96%
 Carpet installation @ library – substantially complete
 Library casework – complete.

Theater (D)

Finish painting - complete
 Acoustical wall panel frames -installed
 Acoustical wall panels at theater – 50% complete
 HVAC equipment (chiller) is in place, piping at pump room – 100% complete – distribution piping – 100%.
 Theater lighting & controls rough ins – substantially complete
 Overhead steel catwalk/spiral stairs work – complete
 HP lifts – 100% installed
 Theater rigging - substantially complete
 Theater seating – 90% complete
 Wood flooring @ small theater – complete
 Main stage /millwork –ongoing – 90% complete
 Carpet at theater – 85% complete
 Stage Flooring – ongoing, 85% complete
 Performance theater – tiered platforms – Substantially complete
 Theater sound/lighting controls- 94% complete
