



Newton North High School

Project Areas by function / Current Construction Activity 05/07/10

Site work – General Items


Multipurpose field – bleachers completed, scoreboard and goal posts installed – synthetic turf started 5/1/10, 50% complete
 Perimeter sidewalks ongoing – 79% - completed main entry and theater entrance plazas, west side of athletic areas- ongoing
 Tennis Ct area: lighting bases – complete , permanent fence posts started, connecting sidewalks nearing completion, permanent light poles complete. Paving completed at parking area
 Grading and granite curb – Ceremonial Drive – complete. Granite curbing near complete other areas.
 Project temporary offices have been relocated – office trailers removed – grading for soccer field started.
 Spreading of topsoil and Landscaping ongoing throughout the site
 Phase 2 logistics planning - ongoing

Pool/Small gym (B) –

Perimeter roof flashings/ roof edge copings 100%
 Natorium – pool tile installation 75% complete, elevated spectator seating completed.
 Pool Locker room finishes (tile, resinous flooring)- 100% complete
 Small Gym - Wood flooring installation, complete, floor finish complete – line painting ongoing
 Athletic Equip – basketball backboards, divider, scoreboards, public address system - completed at both gyms

Academic (C)

Punch list activities - nearing completion at level 4 and 3, continuing on level 2 and 1.
 HVAC commissioning activity continuing
 Fire Alarm pretesting completed.
 Regulatory inspections started with Newton FD, Elevator Inspector, Plumbing and Electrical inspections etc.
 Misc floor finishes – carpet / VCT substantially complete. Rubber treads and risers at stairways near complete
 Ceiling grid and tile installation – substantially complete.
 Interior glass and glazing - completed
 Resilient flooring/vinyl sheet goods – 99% overall complete
 Final building cleaning - continuing

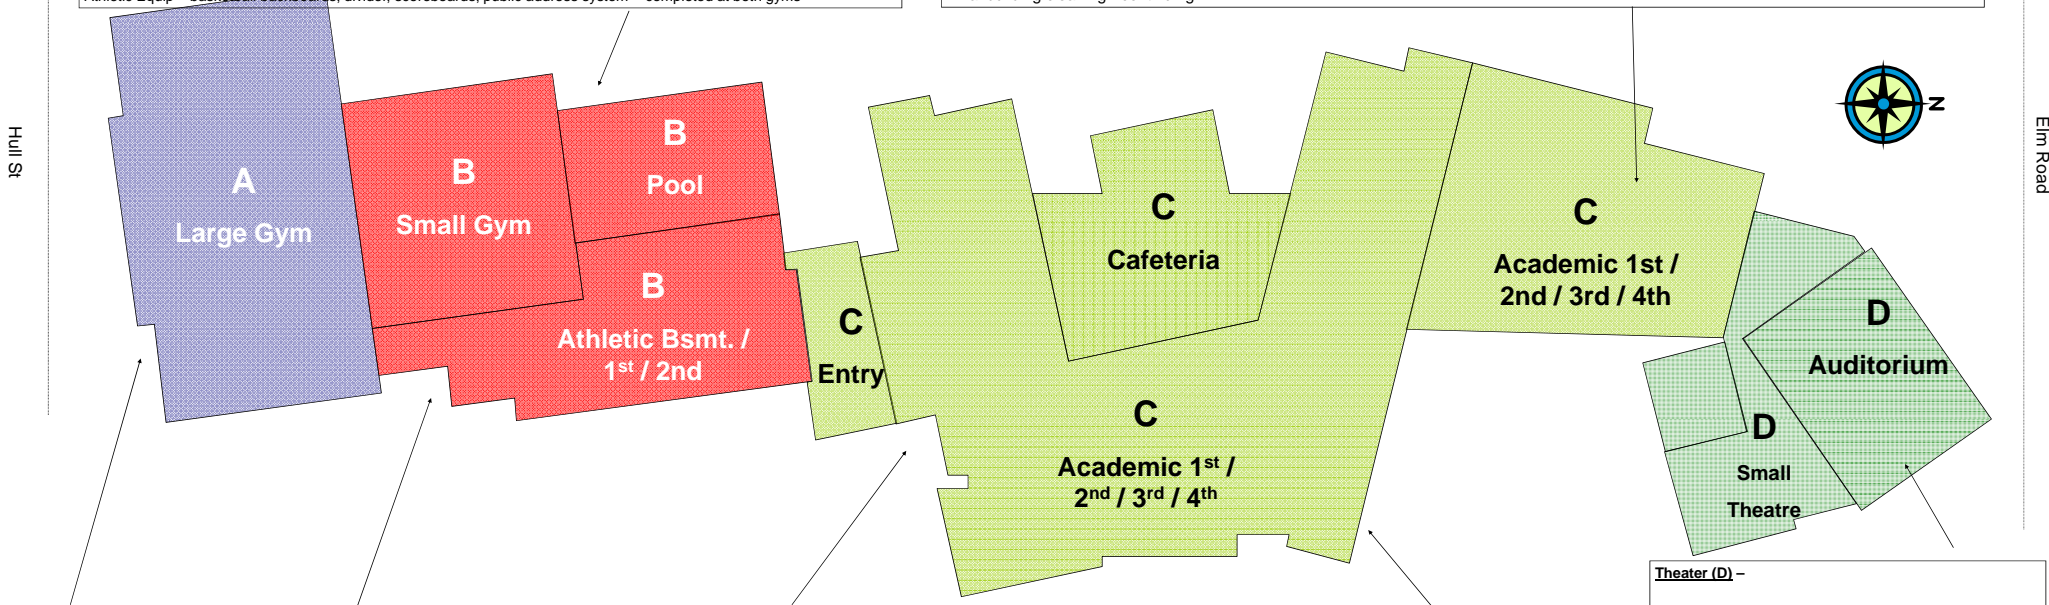

Athletic A, B, Bsmt, Levels 1, 2 & roof:

Athletic equipment/lockers/locker room benches – complete
 Large gym – synthetic flooring completed. Painted game/ track lines – completed
 Remaining metal panels at entry to be delivered mid May
 Aluminum entrances near complete.
 Elevator - temp use certificate received – elevator being utilized for material distribution –Final inspection being scheduled
 Ceramic Tile –basement – completed
 Synthetic flooring, all areas – completed.
 HVAC equipment commissioning - continuing
 Photovoltaic installation at roof: ongoing- 98% complete
 Punchlist activities - started

Academic (C) / Cafeteria (C):

Punch list activities - nearing completion at level 4 and 3, continuing on level 2 and 1.
 HVAC equipment commissioning continuing. Air balancing & Building Management Control system near complete. Owner equipment training – ongoing.
 Fire Alarm pretesting completed. Regulatory inspections started with Newton FD, Elevator Inspector, Plumbing and Electrical inspections etc.
 Painting – completed
 Exterior metal panel work – completed
 Acoustic ceiling grid and ceiling tile – completed
 Food Service equipment – final utility hookups completed
 Final cleaning – interior and exterior - continuing

Theater (D) –

Acoustical wall panel frames -completed
 Acoustical wall panels at theater – 98% complete
 Theater lighting/sound & control devices – substantially complete
 Overhead steel catwalk /spiral stairs work – complete
 HP lifts – 100% installed – inspections scheduled
 Theater rigging - complete
 Theater seating – completed
 Main stage /millwork –completed
 Carpet at theater – 95% complete
 Stage Flooring – complete
 Performance theater – tiered platforms – complete
 Sound/Lighting systems testing – ongoing
 Punch list activity - started
