



Newton North High School

Project Areas by function / Current Construction Activity 05/21/10

Site work – General Items


Multipurpose field – bleachers completed, scoreboard and goal posts installed – synthetic turf started 5/1/10, 95% complete
 Perimeter sidewalks ongoing – 85% - main st entry concrete completed.
 Tennis Ct area: lighting bases – complete ,fencing ongoing, concrete walks complete, court painting started
 Grading and granite curb – Ceremonial Drive – complete. Granite curbing near complete other areas.
 Project temporary offices have been relocated – office trailers removed – grading of soccer field complete, spreading of topsoil ongoing.
 Landscaping ongoing throughout the site – 75% complete
 Phase 2 logistics planning development - ongoing

Pool/Small gym (B) –

Pool water filling and balancing – near complete. Pool accessories installation - ongoing
 Natatorium – pool tile installation 94% complete.
 Pool Locker room finishes (tile, resinous flooring)- 100% complete
 Small Gym - Wood flooring installation, complete, floor finish complete – line painting completed. Bleacher installation to be complete end of week.

Academic (C)

Punch list activities - nearing completion at level 4 and 3, continuing on level 2 and 1.
 HVAC commissioning activity continuing – expected completion June 1
 Fire Alarm NFD testing near complete.
 Regulatory inspections near complete with Newton FD, Elevator Inspector, Plumbing and Electrical inspections etc.
 Misc floor finishes – carpet / VCT complete. Rubber treads and risers at stairways complete
 Resilient flooring/vinyl sheet goods – 100% overall complete
 Final building cleaning - continuing

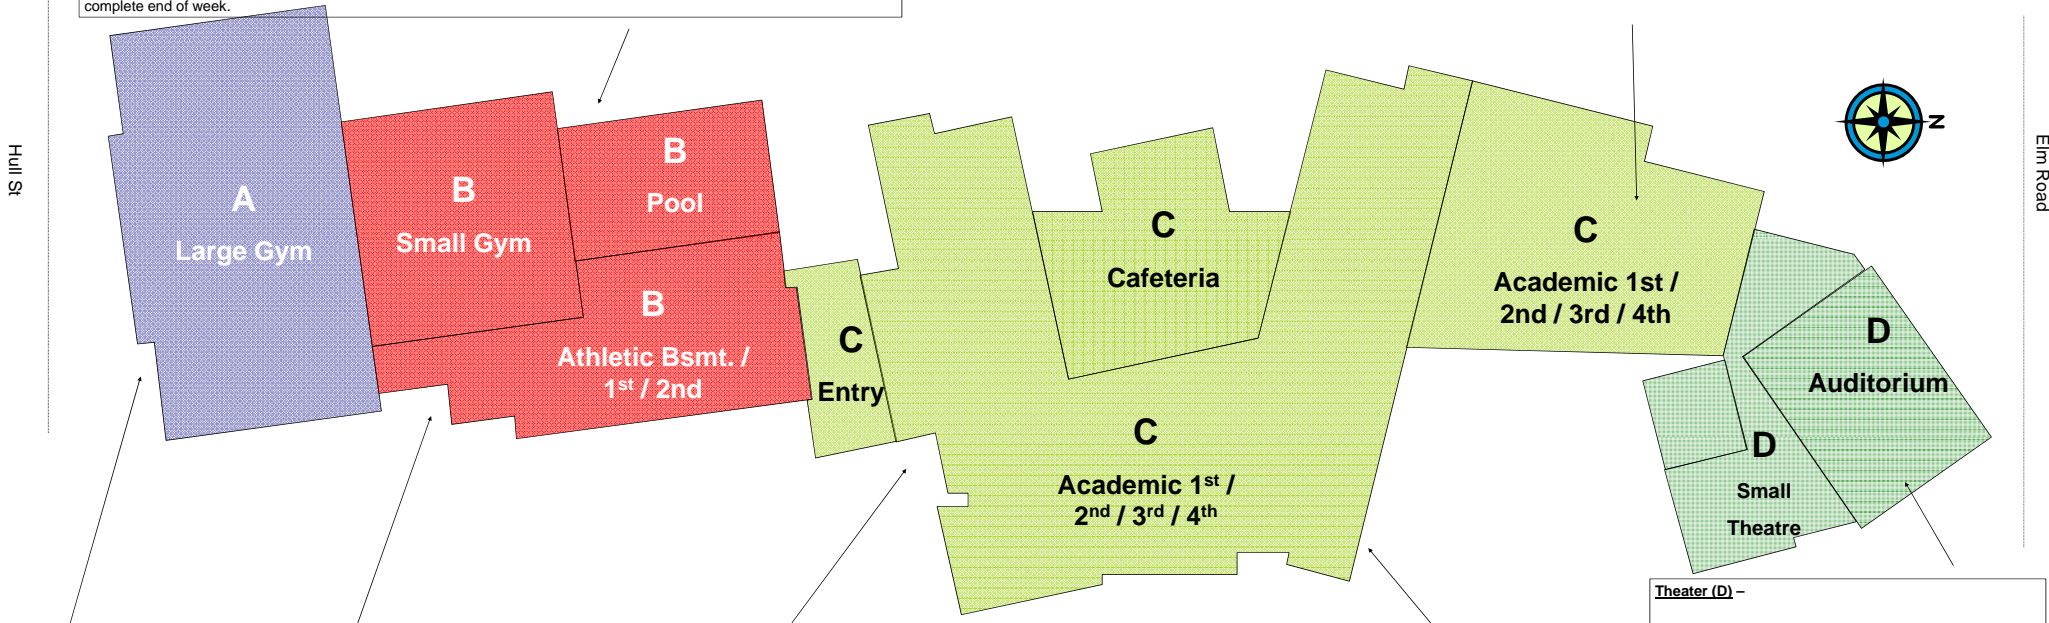

Athletic A, B, Bsmt, Levels 1, 2 & roof:

Athletic equipment/lockers/locker room benches – complete
 Large gym – synthetic flooring completed. Painted game/ track lines – completed
 Remaining metal panels at entry to be delivered mid May
 Aluminum entrances near complete.
 Elevator - temp use certificate received – elevator being utilized for material distribution –Final inspection being scheduled
 Ceramic Tile –basement – completed
 Synthetic flooring, all areas – completed.
 HVAC equipment commissioning - continuing
 Photovoltaic installation at roof: ongoing- 98% complete
 Punchlist activities - started

Academic (C) / Cafeteria (C):

Punch list activities - nearing completion at level 4 and 3, continuing on level 2 and 1.
 HVAC equipment commissioning continuing. Air balancing & Building Management Control system near complete. Owner equipment training – ongoing. Commissioning completion expected June 1
 Fire Alarm NFD testing near complete.
 Regulatory inspections near complete with Newton FD, Elevator Inspector, Plumbing and Electrical inspections etc.
 Painting – punch list ongoing
 Exterior metal panel work – completed
 Acoustic ceiling grid and ceiling tile – completed
 Food Service equipment – final utility hookups completed – Newton Health Dept approval recieved
 Final cleaning – interior and exterior - continuing

Theater (D) –

Acoustical wall panel frames -completed
 Acoustical wall panels at theater – 98% complete
 Theater lighting/sound & control devices – complete
 Overhead steel catwalk /spiral stairs work – complete
 HP lifts – 100% installed – inspections approved
 Main stage /millwork –completed
 Carpet at theater – completed
 Stage Flooring – complete
 Performance theater – tiered platforms – complete
 Sound/Lighting systems testing – complete
 Punch list activities - ongoing
